




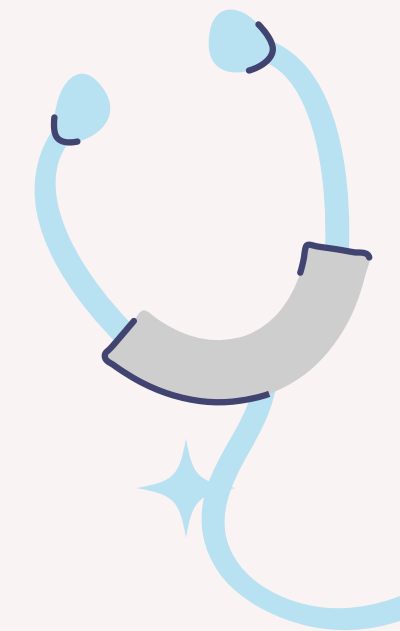

University of Bahrain
College of Information Technology
Department of Information Systems

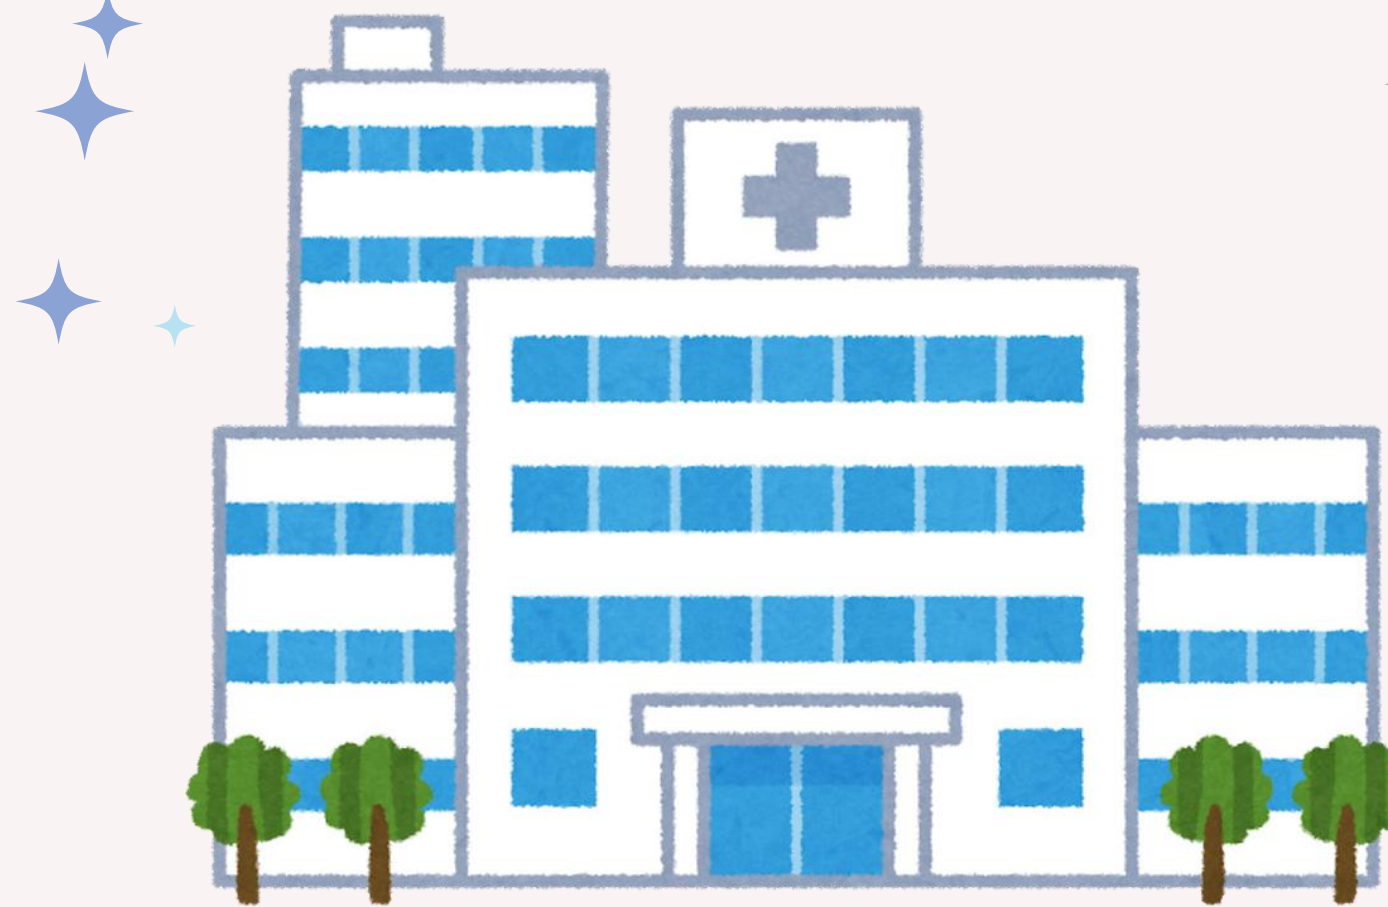

Telemedicine Platform

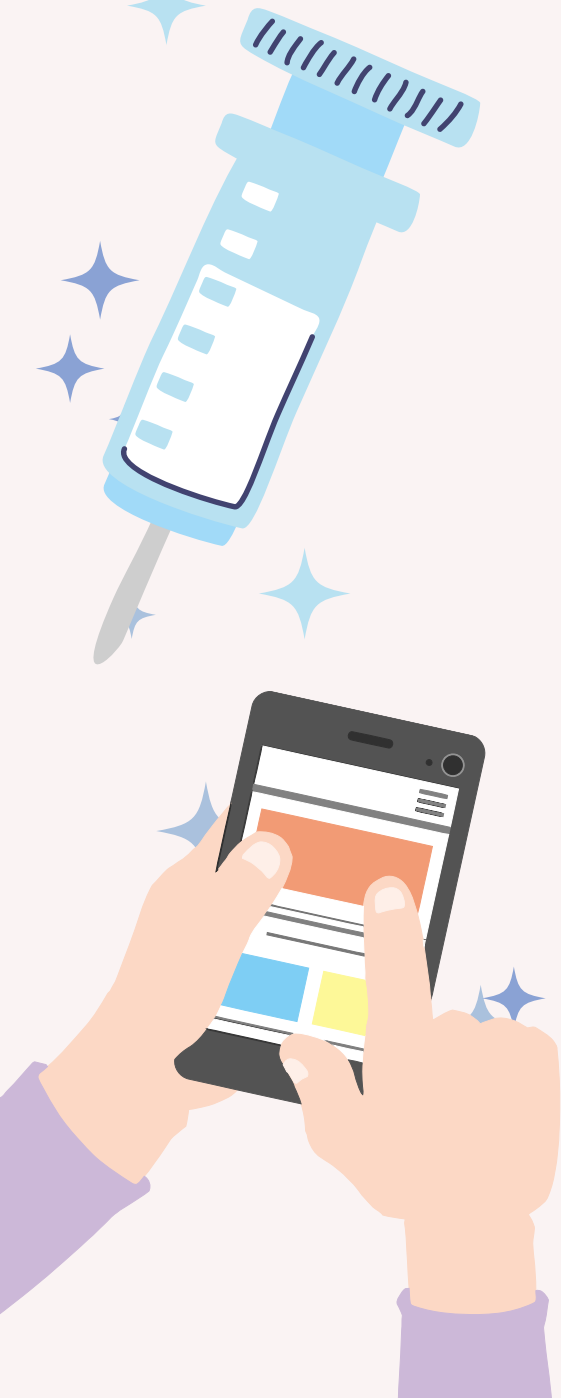

Done By:

Dana Hussain Alhayki -202203431
Aljazi Ali Almujaaddam - 202202227
Noora Abdulrahman Bumajaid - 202203245
Manar Hussain Abdulrahim - 202201554

The Contents:

-01-

**Project
Charter**

-02-

**Stakeholder
Register**

-03-

**Project
Organization**

-04-

**Work Breakdown
Structure
(WBS)**

-05-

**Gantt
Chart**

-06-

**Cost
Estimates**

-07-

**Risk
Register**

-08-

**Risk
Matrix**

-09-

**Communication
management
plan**

-10-

**Lesson
Learned**

-01- Project Charter

1.0 PROJECT IDENTIFICATION	
Name	Telemedicine Platform
Description	City Hospital plans to address the transportation barriers and long distances faced by some residents by developing a telemedicine platform. The project is estimated to cost \$2 million and has a tight implementation timeline of 12 months. The goal is to reduce waiting times for appointments and enhance patient satisfaction.
Sponsor/Owner	Aljazi Ali the CEO of City Hospital and the sponsor
Project Manager	Dana Hussain
Start Date	1/1/2025
End Date	1/1/2026

2.0 BUSINESS REASONS FOR PROJECT
The following are the project's business justifications: 1. Some locals have trouble getting around and must travel great distances to see professionals. 2. Long appointment wait times can have a detrimental impact on patient satisfaction. 3. Appointments can only be made in person at the hospital by patients. 4. Doctors need to make in-person, real-time appointments to perform consultations, diagnose specific diseases, and prescribe medication exclusively in hospitals.

3.0 PROJECT OBJECTIVES (PURPOSE)
1. Improve Access: Enable patients to consult with doctors remotely, overcoming transportation barriers and long distances. 2. Reduce Wait Times: Streamline appointment scheduling and provide timely consultations, minimizing wait times. 3. Enhance Patient Satisfaction: Offer convenient and efficient healthcare services, leading to higher patient satisfaction. 4. Increase Specialist Availability: Facilitate access to specialists by leveraging telemedicine technology. 5. Financial Viability: Execute the project within the estimated budget of \$2 million.

4.0 PROJECT SCOPE
1. Develop a secure and user-friendly telemedicine platform. 2. Integrate the platform with City Hospital's existing electronic medical record system. 3. Launch the platform and provide ongoing support and maintenance. 4. enables video conferencing for remote patient-doctor consultations. 5. Without having to go to the hospital, users can use the platform to make appointments with professionals for consultations.

5.0 KEY PROJECT DELIVERABLES	
Name	Description
Patient appointment scheduling system	<i>The project deliverable includes a feature that enables patients to conveniently schedule appointments with specialists using the telemedicine platform, eliminating the necessity for in-person visits to the hospital and enhancing accessibility to healthcare services.</i>
Integration with electronic medical records	An important deliverable of the project is the smooth integration of the platform with the hospital's electronic medical records system, allowing doctors to conveniently access patient history and pertinent medical information during virtual visits, thereby ensuring uninterrupted and consistent healthcare.

Secure and private video conferencing technology	The project deliverable involves the use of secure video conferencing technology within the telemedicine platform to safeguard patient privacy and ensure data security during remote consultations.
Improved healthcare delivery efficiency	A key objective of the project is to improve the efficiency of healthcare delivery by enabling doctors to remotely attend to a greater number of patients, thereby optimizing their time and resources
Patient Satisfaction	As part of the project, the platform should provide educational resources and send appointment reminders to actively engage patients in their healthcare, fostering awareness, self-care, and ultimately leading to improved health outcomes

6.0 MILESTONE DATES		
Item	Major Events / Milestones	Dates
1	meeting with the project manager and the sponsor : 1. determine the three constraints time, scope, and cost. 2. collect information, requirements, and resources. 3. determine the salary and role of each team member.	1/1/2025 1/1/2025
2	Planning : 1. Platform interface. 2. plan to control the budget. 3. project team member salary and role	3/1/2025 9/1/2025
3	Front-end Application	15/1/2025 18/4/2025
4	Back-end Application	19/4/2025 20/9/2025
5	Testing the platform and collect feedback	25/9/2025 20/10/2025
6	Edit the last application features and get the last version of the application	23/10/2025 15/12/2025
7	Final meetings to review the final version of the application with all stakeholder	18/12/2025 21/12/2025
8	Close-up the project and submit it	25/12/2025
9	Launching the application to user via application installation program such as app store and google play	25/12/2025 1/1/2026

7.0 Project budget
\$2 million

8.0 RISKS	
Severity	Description
1.high	Security and privacy issues
2.high	Work ethics
3.high	Lack in quality of care and the diagnoses will be limited
4.meduim	Technical issues or system failures could disrupt patient consultations and compromise the effectiveness and reliability of the telemedicine platform.

5.meduim	Integration issues
6.high	Low adoption of using the Application


9.0 SIGNOFF
Project Sponsor:  Date: 8/April/2024



-02- Stakeholder Register

Name	position	Category	Project role	Power (H/L)	Inter est (H/L)	Contact
Patricia Kriston	Financial Analysis	Internal	Financial Controller	H	H	PatriciaKriston@gmail.com
Aljazi Ali	CEO	Internal	Sponsor	H	H	202202227@stu.uob.edu.bh
Dana Hussain	PMO Director	External	Project manager	H	H	202203431@stu.uob.edu.bh
Manar Hussain	PR Director	Internal	Advisor	H	H	202201554@stu.uob.edu.bh
Noora Abdulrahman	Vise President	Internal	Advisor	H	H	202203241@stu.uob.edu.bh
Hanan Rashed	President	Internal	Planner	H	H	HananRashed@gmail.com
Jassim Ahmed	Team Member	External	Backend-Programmer	L	H	JassimAhmed@gmail.com
Khaled Nasser	Team Member	External	Frontend-Programmer	L	H	KhaledNasser@gmail.com
Asmaa Yosif	Team Member	External	Data Analysis	L	L	AsmaaYosif@gmail.com
Hessa Khaled	Team Member	External	Database Administrator	L	L	HessaKhaled@gmail.com
Jalal Ali	Team Member	External	Application Developer	L	H	JalalAli@gmail.com
Abdulrahman Ahmed	Team Member	External	Testing-Application	H	H	AbdulrahmanAhmed@gmail.com
Shaikha Hamad	Head Of Department	Internal	Monitoring and controlling	H	H	ShaikhaHamad@gmail.com
Bader Hassan	Coordinator	Internal	Coordinate	H	H	BaderHassan@gmail.com
Faisal Mohamed	Information Security Manager	Internal	Security Policies	H	H	FaisalMohamed@gmail.com

-03- Project Organization

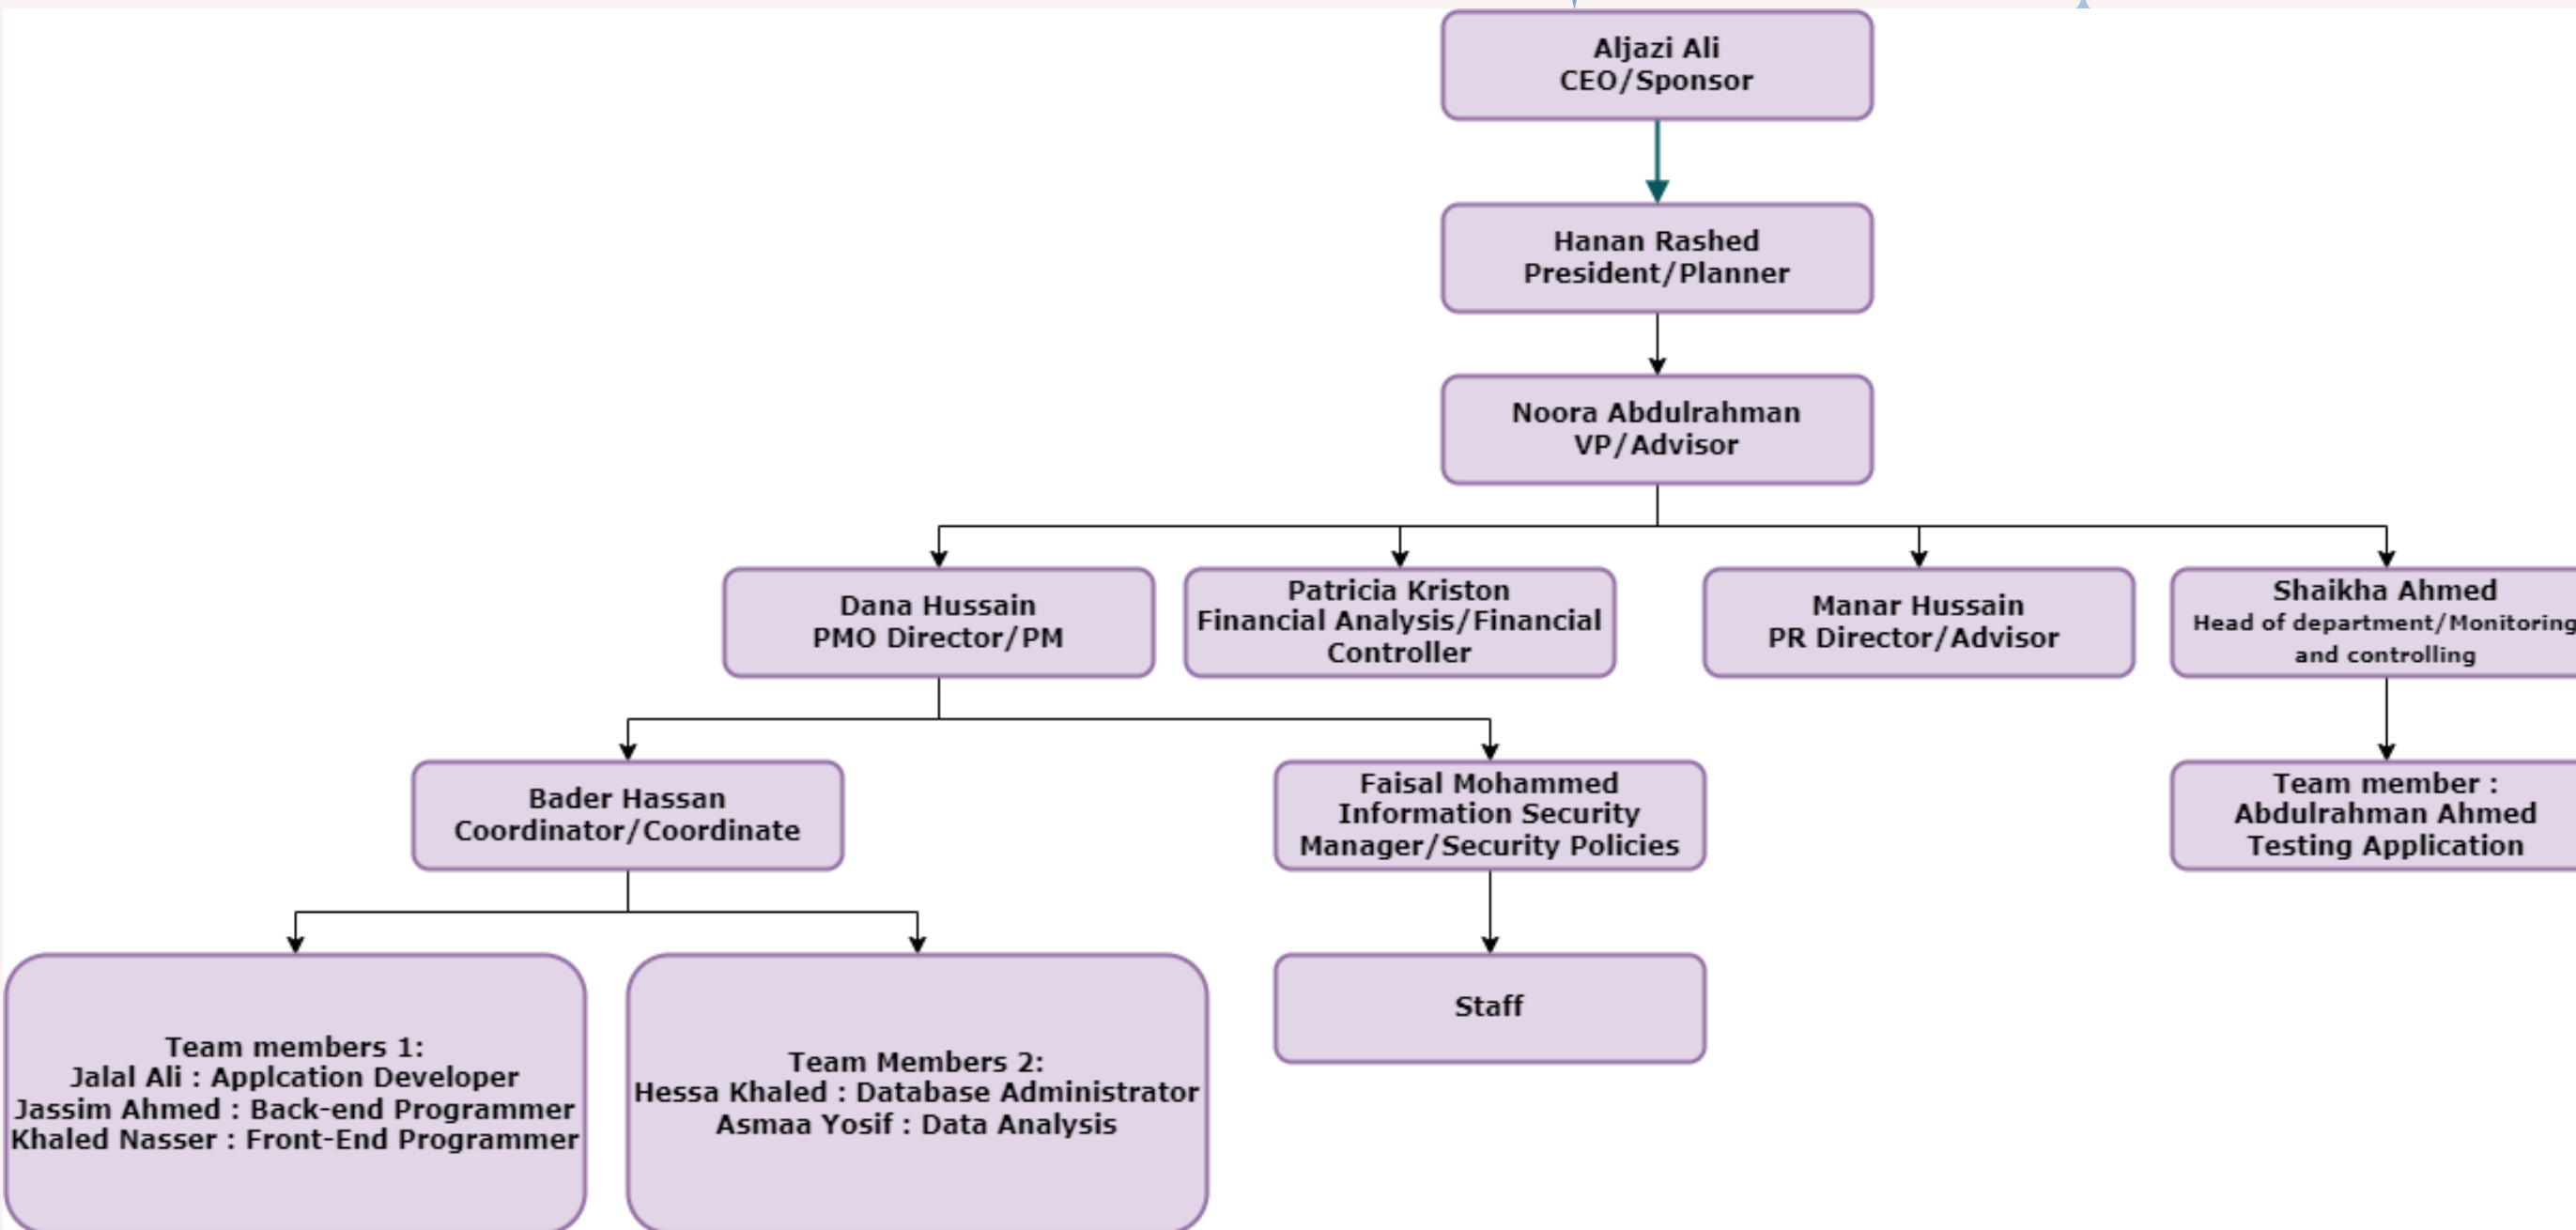


Responsibility Table:

Position	Responsibility
1.CEO/Sponsor	-Provides overall strategic direction and vision for the project. - Acts as the primary sponsor and advocate for the project. - Approves project goals, objectives, and major deliverables.
2. Planner /President	- Develops project plans and schedules. - Identifies project milestones and deliverables. - Coordinates with the project manager and team to ensure timely execution.
3. Vice President/Advisor	-Provides expert advice and guidance on project-related matters. -Assists in developing project strategies and plans. -Evaluates project risks and advises on risk mitigation strategies.

4. Project Manager /PMO Director	- Responsible for overall project management, planning, and coordination. - Acts as the main point of contact for the project team and stakeholders. - Manages project scope, schedule, and budget. - Ensures project objectives are met and delivers successful outcomes.
5. Financial Controller	- Provides financial analysis and oversight for the project. - Manages project budgeting and financial reporting. - Monitors project expenses and ensures financial compliance. - Collaborates with the project manager to make informed financial decisions.
6. Advisor /PR Director and Vice President	- Provides guidance and expertise related to public relations and strategic planning. - Assists in developing project communication strategies and stakeholder engagement. - Offers advice on project direction, goals, and decision-making.
7. Monitoring and Controlling /Head Of Department	- Monitors project progress, performance, and compliance. - Implements controls and processes to ensure project objectives are achieved. - Identifies and mitigates project risks and issues.
8. Coordinator	- Assists in coordinating project activities and resources. - Supports the project manager in administrative tasks. - Communicates and collaborates with team members and stakeholders.
9. Information Security Manager	- Develops and implements project security policies and procedures. - Ensures compliance with data protection regulations. - Manages project security risks and safeguards project assets.


10. Testing-Application	Conducts testing and quality assurance activities for project applications. - Develops test plans and executes test cases. - Reports and tracks defects, working with the development team to resolve issues
11. Application Developer	Develops and maintains project applications and software solutions. - Collaborates with the project team to understand requirements and implement solutions. - Conducts testing and debugging to ensure application functionality
12. Backend Programmer	- Responsible for developing and maintaining the backend systems and infrastructure. - Collaborates with frontend programmers and other team members to integrate systems. - Ensures the backend functionality aligns with project requirements.
13. Frontend Programmer	Develops and maintains the user interface and frontend components of the project. - Collaborates with backend programmers and other team members for seamless integration. - Implements user experience (UX) design and ensures responsive and intuitive interfaces.
14. Database Administrator	- Manages the project's databases and data storage systems. - Ensures data integrity, security, and availability. - Optimizes database performance and troubleshoots issues.
15. Data Analyst	- Conducts data analysis and provides insights for decision-making. - Cleans and analyzes project data to identify trends, patterns, and opportunities. - Collaborates with the project team to optimize data-driven strategies.


-04- The Work Breakdown Structure (WBS):

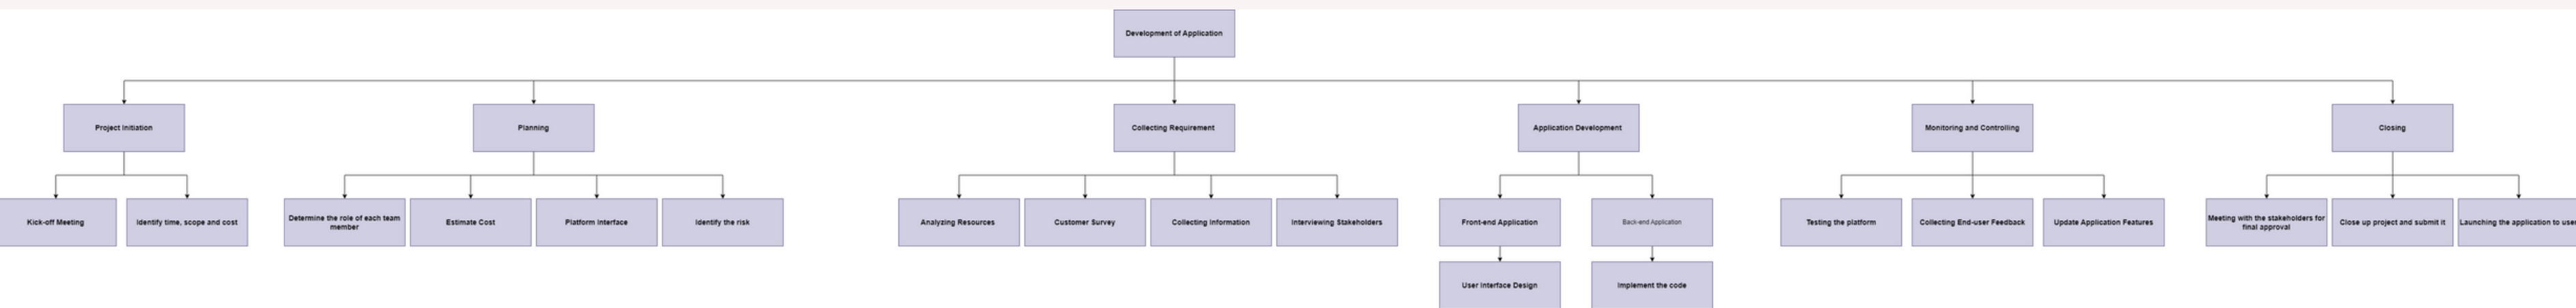

-05-

Gantt chart

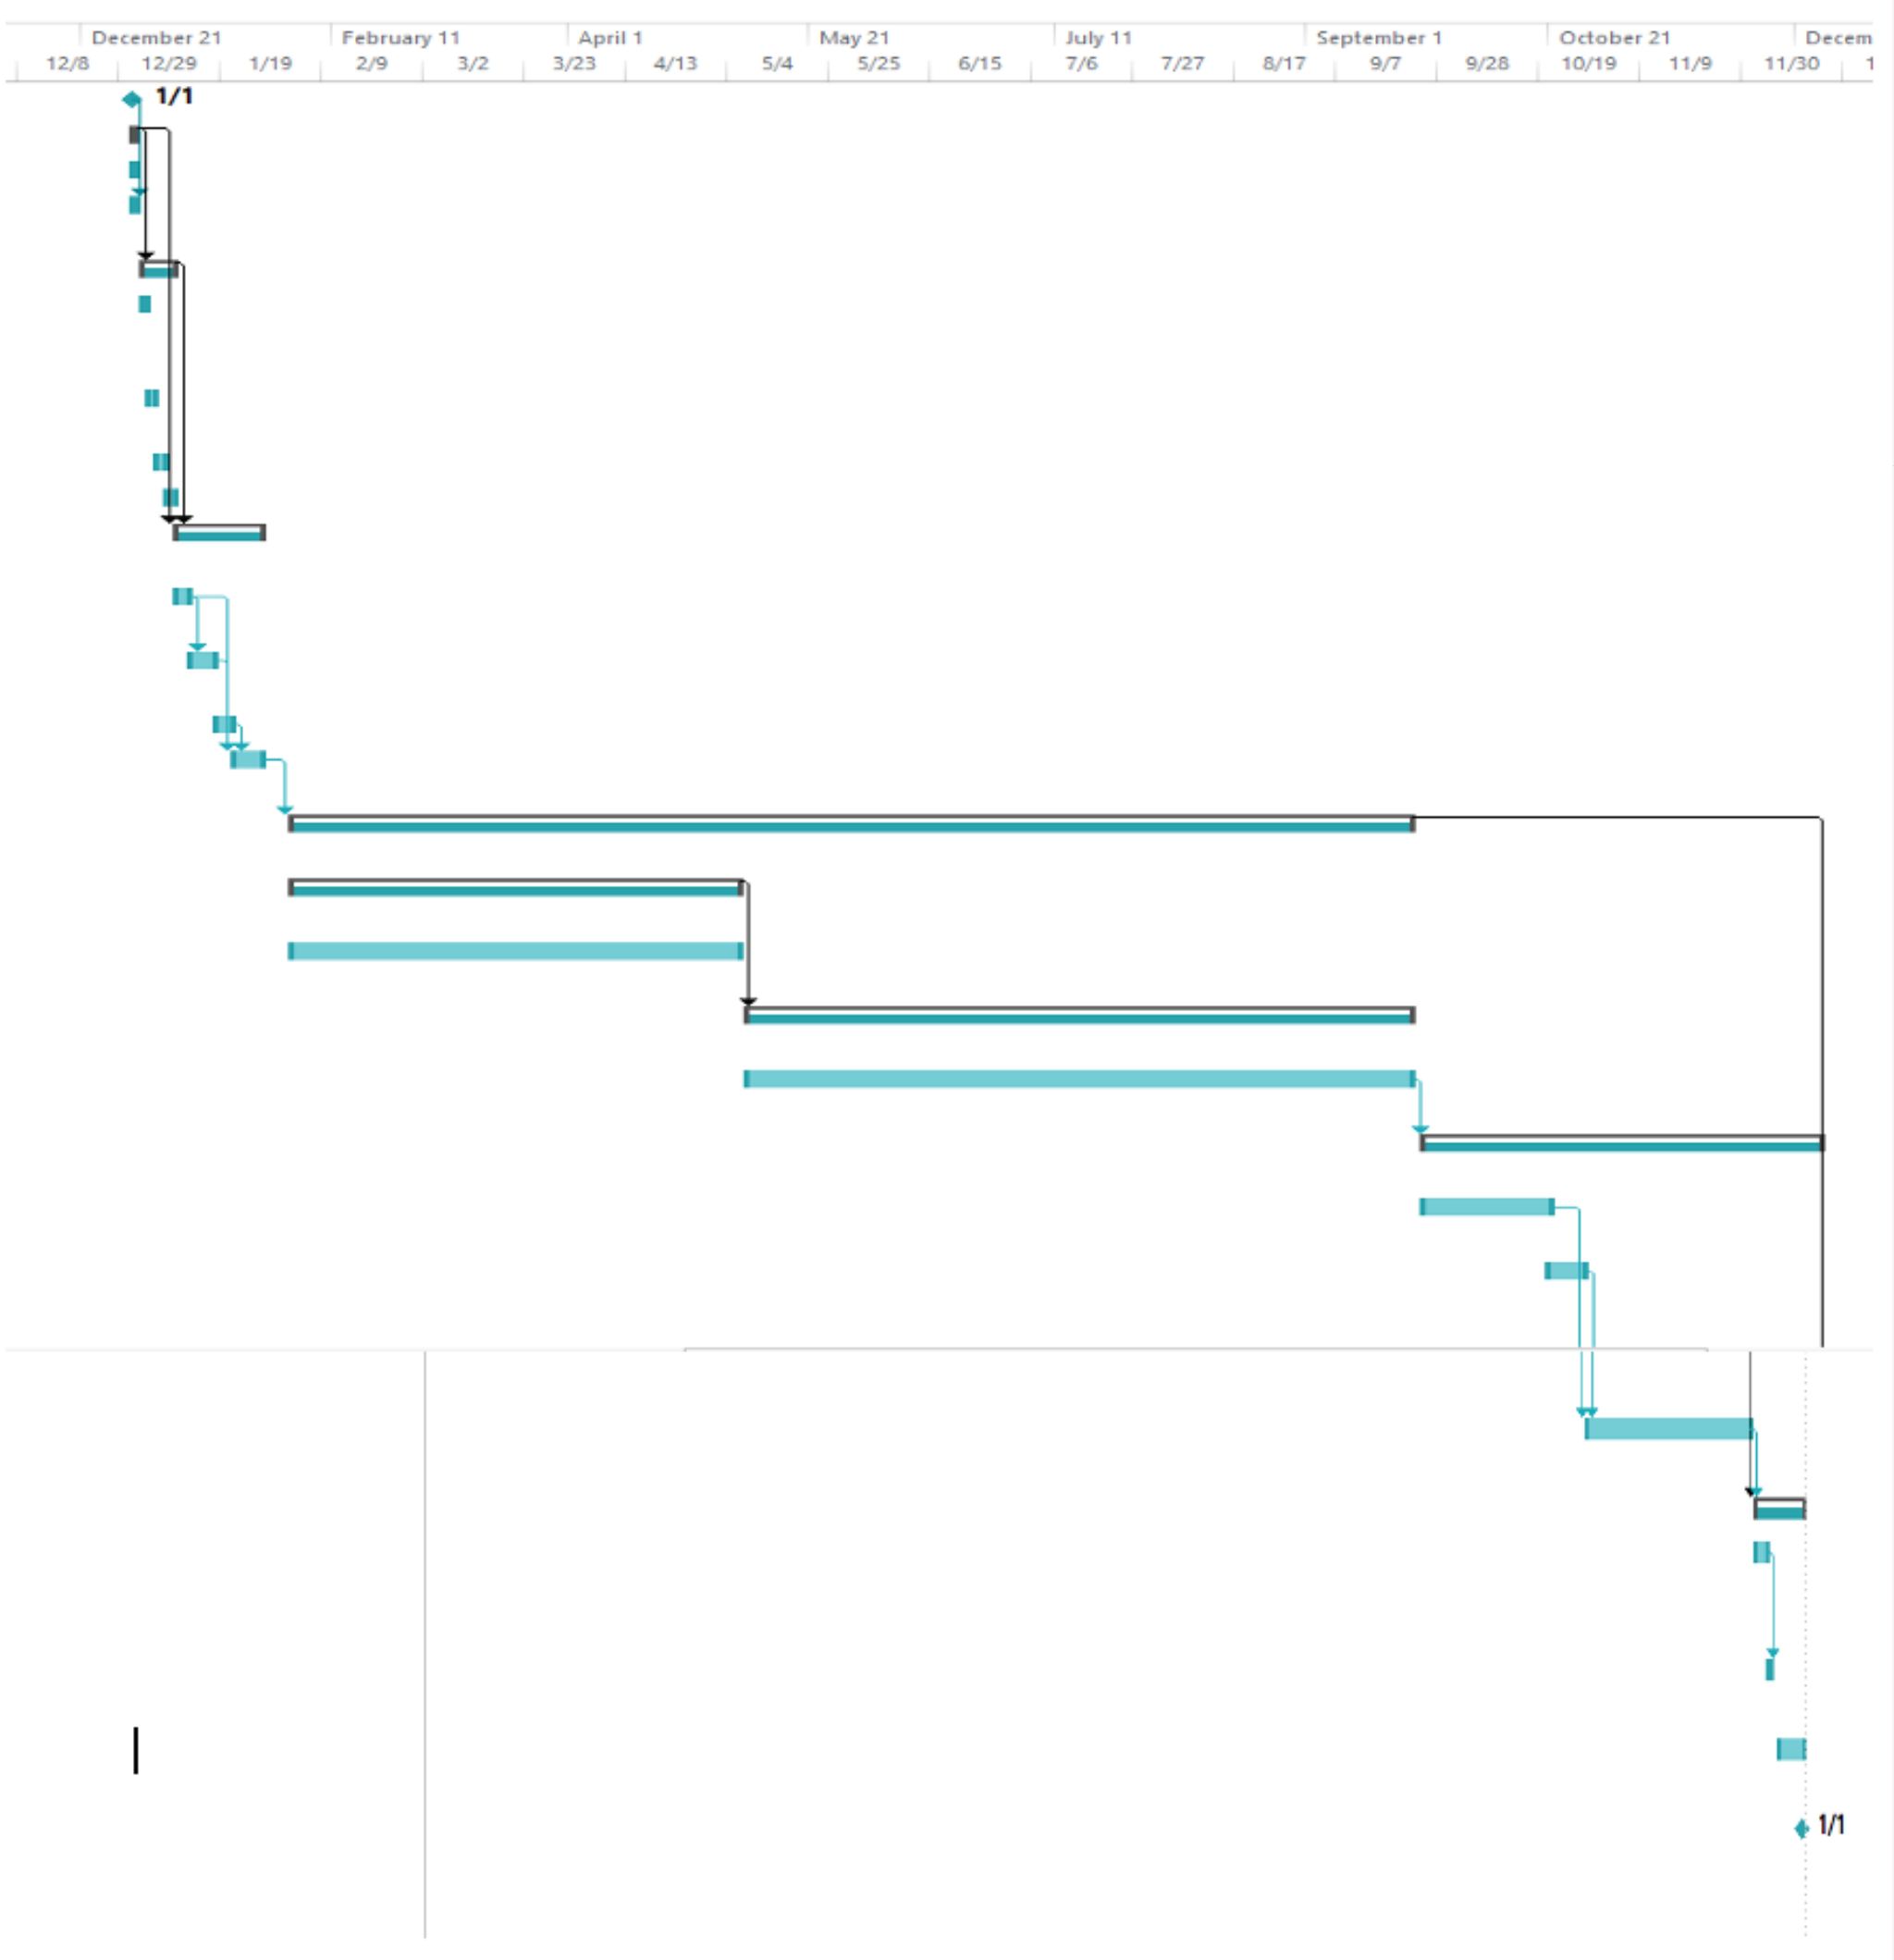


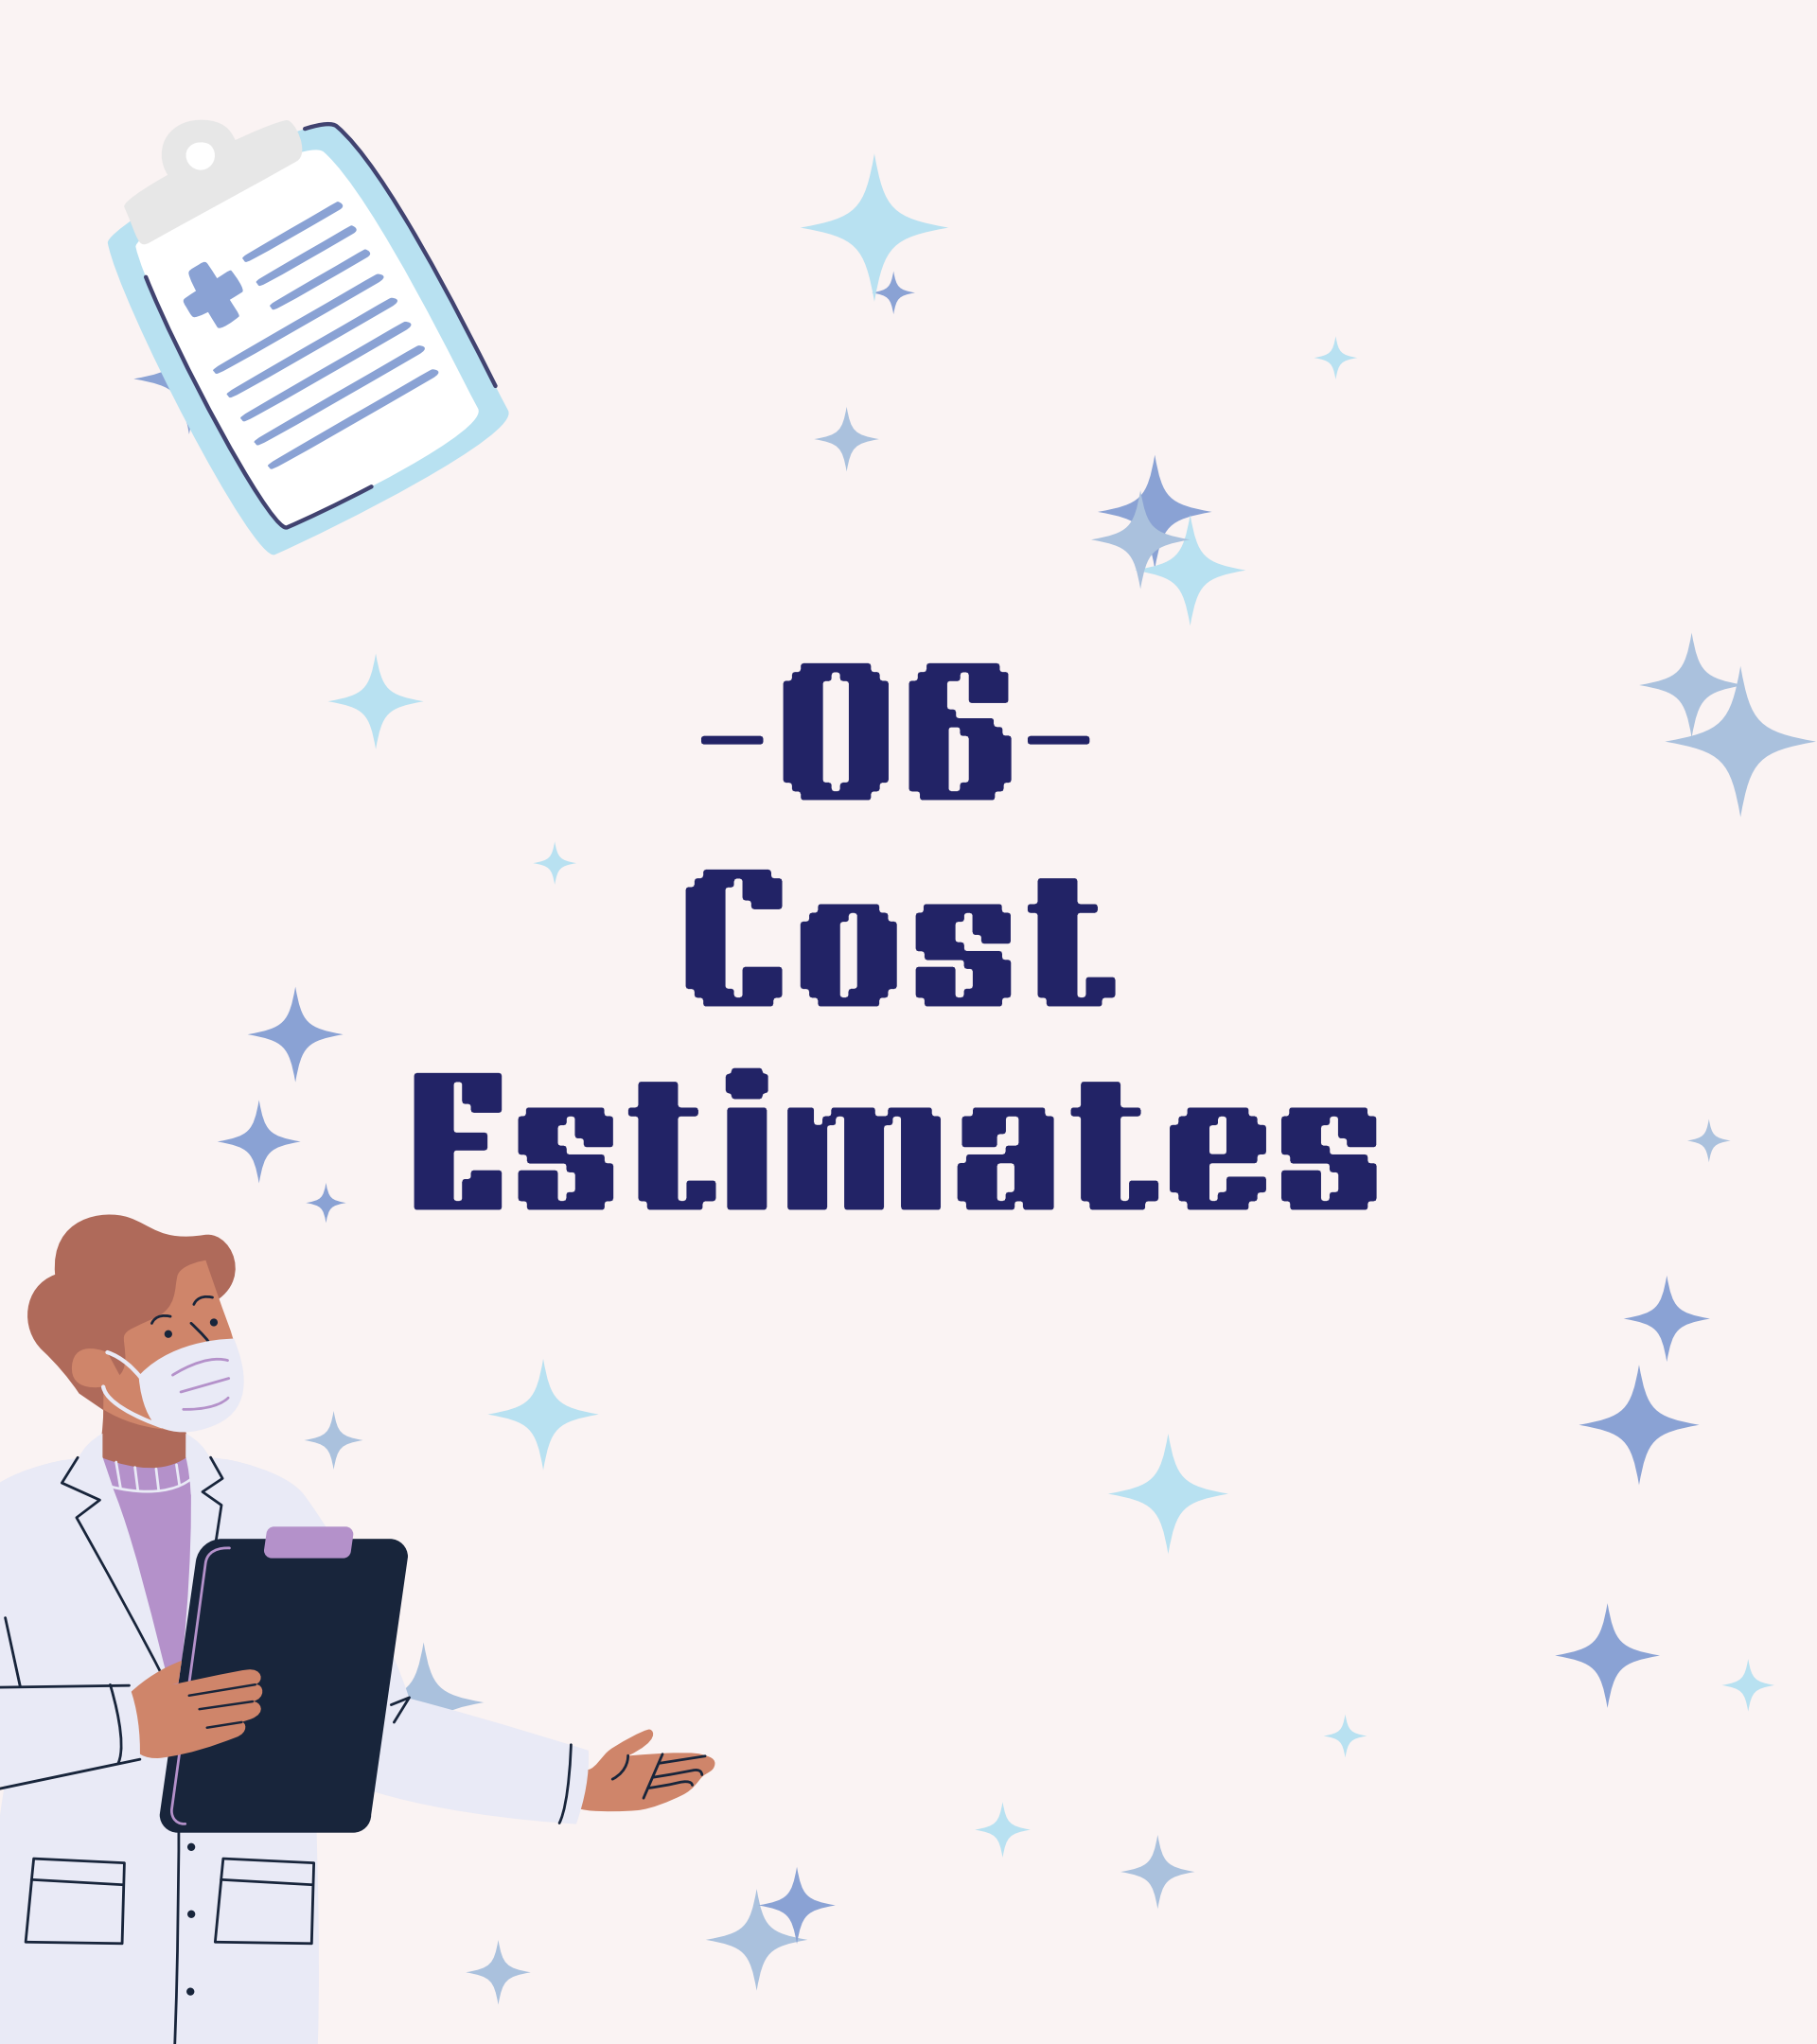

-06- Cost Estimates

	#Units/Hrs.	Cost/Units/Hrs.	Subtotals	WBS level 1 Totals	% Of total
1 Project Initiation				\$800	0.04%
1.1 Kick-off Meeting	3	\$200	\$600		
1.2 Identify time, <u>scope</u> and cost	4	\$50	\$200		
2 Planning				\$76,500	3.825%
2.1 Determine the role of each team member	5	\$100	\$500		
2.2 Platform Interface	16	\$2,000	\$32,000		
2.3 Estimate Cost	10	\$2,000	\$20,000		
2.4 Identify the risk	12	\$2,000	\$24,000		
3 Collecting Requirements				\$24,400	1.22%
3.1 Interviewing Stakeholders	8	\$200	\$1,600		
3.2 Collecting Information	32	\$300	\$9,600		
3.3 Customer Survey	24	\$50	\$1,200		
3.4 Analyzing Resources	30	\$400	\$12,000		
4 Application Development				\$1,020,000	51%
4.1 Front-end Application				\$300,000	
4.1.1 User Interface Design	500	\$600	\$300,000		
4.2 Back-end Application				\$720,000	
4.2.1 Implement the code	720	\$1,000	\$720,000		
5 Monitoring and Controlling				\$32,350	1.6175%
5.1 Testing the platform	120	\$100	\$12,000		
5.2 Collecting End-user Feedback	40	\$40	\$1,600		
5.3 Update Application Features	250	\$75	\$18,750		
6 Closing				\$83,240	4.162%
6.1 Meeting with the stakeholders for final approval	15	\$200	\$3,000		
6.2 Close up project and submit it	8	\$30	\$240		
6.3 Launching the application to user	40	\$2,000	\$80,000		
6.4 Project Closure					
Reserves				\$762,710	38.1355%
Total Project Cost Estimate				\$1,237,290	61.8645%


-07- Risk Register

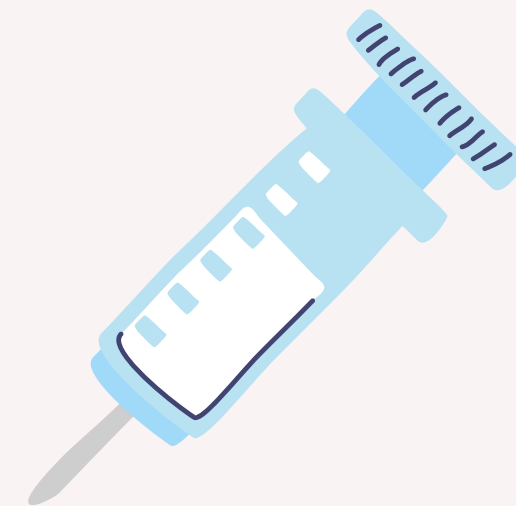

No.	Rank	Risk	Description	Category	Root Cause	Triggers	Potential Responses	Risk Owner	Probability	Impact	Status
R1	1	Work Ethics	Ethical issues related to work practice or behaviour	Organizational	Lack of clear ethical guidelines or enforcements	Unethical behavior by employees	Establish and enforce clear ethical guidelines, provide ethics training	Human Resources	Medium	High	Ongoing
R2	2	Security and Privacy Issues	Breaches of security and privacy of user data	Technical	Inadequate security measures or vulnerabilities	Hacking attempts, data leaks	Strengthen security measures, implement encryption and access controls	IT Department	Low	High	Mitigated
R3	3	Lack of Quality of Care and Limited Diagnosis	Insufficient quality of care and limited diagnostic capabilities	Operational	Inadequate training or resources for healthcare professionals	Misdiagnosis, inadequate treatment	Improve training programs, invest in advanced diagnostic tools	Healthcare Management	High	Medium	In progress
R4	4	Low Adaption of using the Application	Limited user adaption and engagement with the application	Organizational	Lack of awareness or understanding of the benefits	Resistance to change, lack of user-friendly interface	Conduct awareness campaigns, improve user interface and user experience	Marketing Department	Medium	Medium	Ongoing
R5	5	Technical Issues or System Failures	Malfunctions or failures in the application or system	Technical	Software bugs, hardware failures	Application crashes, system downtime	Regular maintenance, bug fixing, backup systems	IT Department	High	High	Open
R5	6	Integration Issues	Challenges in integrating the application with existing systems	Technical	Incompatibility with legacy systems, lack of interoperability	Data synchronization issues and data loss	Conduct compatibility assessments, develop integration protocols	IT Department	Low	Medium	Resolved

-08- Risk Matrix

probability	High		Risk 3 - Lack of Quality of Care and Limited Diagnosis	Risk 5 - Technical Issues or System Failures
	medium		Risk 4 - Low Adaption of using the Application	Risk 1 - Work Ethics
	Low		Risk 6 - Integration Issues	Risk 2 - Security and Privacy Issues
		Low	Medium	High
		impact		

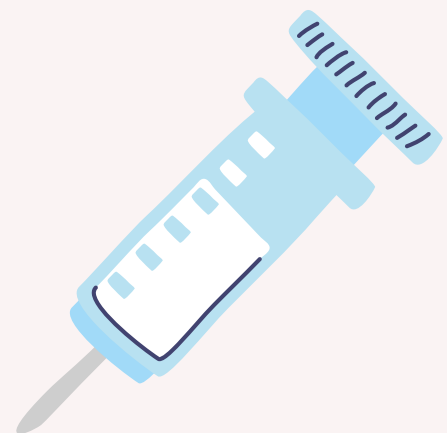

-09- Communication management plan


Stakeholder Identification	Communication Objectives	Communication Channel	Communication Frequency	Communication Methods	Escalation procedure	Communication Responsibilities	Communication Evaluation	Contact Information
Aljazi Ali (Sponser)	- Provide project vision and strategic guidance. - Stay informed about project progress and milestones. - Address escalated issues and make key decisions.	Email: Primary mode of communication for high-level project updates, strategic guidance, and addressing escalated issues.	- Monthly updates on project status and achievements. - Ad hoc communication as required for urgent matters or stakeholder requests	- Monthly Project Updates: Detailed reports highlighting project achievements, challenges, and upcoming milestones. - One-on-One Meetings: Scheduled meetings to discuss project progress, address concerns, and seek strategic input	Aljazi Ali can escalate any significant project-related issues or concerns to the Project Manager (Dana Hussain) or involve higher-level stakeholders, such as the President (Hanan Rashed).	Review project updates, provide strategic guidance, and make informed decisions.	The effectiveness of communication channels and their alignment with strategic objectives	202202227@stu.uob.edu.bh
Dana Hussain (Project Manager)	- Facilitate effective communication among all stakeholders. - Share project progress, updates, and milestones. - Address and resolve issues raised by stakeholders.	Email: Primary mode of communication for project updates, task assignments, and addressing stakeholder concerns.	- Weekly project team meetings. - Monthly stakeholder updates. - Ad hoc communication as required to address urgent matters or specific stakeholder requests.	- Project Team Meetings: Weekly meetings to discuss progress, address issues, and assign tasks. - Stakeholder Updates: Monthly reports highlighting project status, achievements, and upcoming activities. - Ad hoc Communication: Additional meetings or communications as required to address urgent matters or specific stakeholder requests	- If any stakeholder has an issue or concern that cannot be resolved at the project team level, they can escalate it to Dana Hussain. - Dana will review the issue, involve relevant stakeholders, and work towards resolving it in a timely manner. - If the issue remains unresolved, Dana will escalate it to the Project Sponsor (Aljazi Ali) for further action and decision-making.	Responsible for overall communication management, including preparing and disseminating project updates, conducting meetings, and addressing stakeholder concerns	Feedback from stakeholders regarding the effectiveness of communication channels and Dana's communication approach.	202203431@stu.uob.edu.bh
Patricia Kriston (Financial Controller)	- Share financial analysis reports and updates. - Discuss budgetary matters and financial forecasts. - Address any financial concerns or queries.	Email: The primary mode of communication for formal project updates, reports, and financial-related discussions.	- Monthly financial reports and updates. - Ad hoc communication as required or for urgent financial matters	- Formal Financial Reports: Detailed reports on financial analysis, budget status, and forecasts. - Email Updates: Regular email updates on financial matters and any urgent financial-related information.	If Patricia encounters any financial issues or requires additional support, she can escalate them to the Project Manager (Dana Hussain) or the Project Sponsor (Aljazi Ali) for assistance	Actively participate in project meetings, provide input on financial matters, and communicate any concerns promptly.	The effectiveness of financial communication channels and opportunities for improvement.	PatriciaKriston@gmail.com
Manar Hussain (PR Director)	- Share PR strategies and updates. - Coordinate PR campaigns and activities. - Address any PR-related concerns or queries.	Email: Primary mode of communication for PR-related updates, campaigns, and coordination	- Monthly PR updates. - Ad hoc communication as required for urgent PR matters	- PR Campaign Reports: Detailed reports on PR campaigns, media coverage, and public perception. - Email Updates: Regular email updates on PR activities, upcoming events, and any urgent PR-related information	If Manar encounters any significant PR issues or requires additional support, she can escalate them to the Project Manager (Dana Hussain) or the Project Sponsor (Aljazi Ali) for assistance	Actively participate in project meetings, provide input on PR matters, and communicate any concerns or updates promptly.	The effectiveness of PR communication channels and opportunities for improvement	202201554@stu.uob.edu.bh

Noora Abdulrahman (Vice President)	- Provide strategic guidance and input. - Stay informed about project progress and milestones. - Address escalated issues and make key decisions.	Email: Primary mode of communication for high-level project updates, strategic guidance, and addressing escalated issues.	- Monthly updates on project status and achievements. - Ad hoc communication as required for urgent matters or stakeholder requests	- Monthly Project Updates: Detailed reports highlighting project achievements, challenges, and upcoming milestones. - One-on-One Meetings: Scheduled meetings to discuss project progress, address concerns, and seek strategic input	scalate any significant project-related issues or concerns to the Project Manager (Dana Hussain) or involve higher-level stakeholders, such as the President (Hanan Rashed).	Review project updates, provide strategic guidance, and make informed decisions.	Regarding the effectiveness of communication channels and their alignment with strategic objectives.	202203241@stu.uob.edu.bh
Hanan Rashed (President)	Provide overall project direction and leadership. Stay informed about project progress and achievements. Address escalated issues and make key decisions.	Email: Primary mode of communication for high-level project updates, strategic guidance, and addressing escalated issues.	Monthly updates on project status and achievements. Ad hoc communication as required for urgent matters or stakeholder requests.	Monthly Project Updates: Detailed reports highlighting project achievements, challenges, and upcoming milestones. One-on-One Meetings: Scheduled meetings to discuss project progress, address concerns, and seek strategic input.	Hanan Rashed can be involved in escalated matters or decisions that require the President's attention and approval.	Hanan Rashed: Review project updates, provide strategic guidance, and make informed decisions.	Feedback from Hanan Rashed regarding the effectiveness of communication channels and their alignment with strategic objectives.	HananRashed@gmail.com
Jassim Ahmed (Team Member - Backend Programmer)	Collaborate with the team on backend development tasks. Provide updates on progress and raise any technical concerns	Team Collaboration Platform: Primary mode of communication for task assignments, progress updates, and technical discussions.	Daily stand-up meetings. Ad hoc communication as required for task coordination and issue resolution.	Team Collaboration Platform: Discussions, task updates, and file sharing. Daily Stand-up Meetings: Brief updates on progress, challenges, and plans for the day.	Jassim can escalate any significant technical issues or concerns to the Project Manager (Dana Hussain) or the Technical Lead (Jalal Ali) for assistance.	Jassim Ahmed: Actively participate in team meetings, provide updates on backend development, and communicate any technical concerns promptly.	Feedback from Jassim regarding the effectiveness of communication channels and opportunities for improvement.	JassimAhmed@gmail.com
Khaled Nasser (Team Member - Frontend Programmer)	Collaborate with the team on frontend development tasks. Provide updates on progress and raise any technical concerns.	Team Collaboration Platform: Primary mode of communication for task assignments, progress updates, and technical discussions.	Daily stand-up meetings. Ad hoc communication as required for task coordination and issue resolution.	Team Collaboration Platform: Discussions, task updates, and file sharing. Daily Stand-up Meetings: Brief updates on progress, challenges, and plans for the day.	Khaled can escalate any significant technical issues or concerns to the Project Manager (Dana Hussain) or the Technical Lead (Jalal Ali) for assistance.	Khaled Nasser: Actively participate in team meetings, provide updates on frontend development, and communicate any technical concerns promptly	Feedback from Khaled regarding the effectiveness of communication channels and opportunities for improvement.	KhaledNasser@gmail.com
Asmaa Yosif (Team Member - Data Analysis)	Collaborate with the team on data analysis tasks. Provide updates on analysis progress and insights.	Team Collaboration Platform: Primary mode of communication for task assignments, data analysis updates, and discussions.	Weekly data analysis meetings. Ad hoc communication as required for task coordination and data-related discussions.	Team Collaboration Platform: Discussions, task updates, and file sharing. Weekly Data Analysis Meetings: Detailed updates on analysis progress, findings, and challenges	Asmaa can escalate any significant data analysis issues or concerns to the Project Manager (Dana Hussain) or the Data Analysis Lead for assistance.	Asmaa Yosif: Actively participate in data analysis meetings, provide updates on analysis progress, and communicate any data-related concerns promptly.	Feedback from Asmaa regarding the effectiveness of communication channels and opportunities for improvement.	AsmaaYosif@gmail.com

Hessa Khaled (Team Member - Database Administrator)	Collaborate with the team on database administration tasks. Provide updates on database configurations and maintenance.	Team Collaboration Platform: Primary mode of communication for database-related tasks, updates, and discussions	Weekly database administration meetings. Ad hoc communication as required for task coordination and database-related discussions.	Team Collaboration Platform: Discussions, task updates, and file sharing. Weekly Database Administration Meetings: Detailed updates on database configurations, maintenance, and challenges.	Hessa can escalate any significant database administration issues or concerns to the Project Manager (Dana Hussain) or the Database Administration Lead for assistance.	Hessa Khaled: Actively participate in database administration meetings, provide updates on database tasks, and communicate any database-related concerns promptly.	Feedback from Hessa regarding the effectiveness of communication channels and opportunities for improvement.	HessaKhaled@gmail.com
Jalal Ali (Team Member - Application Developer)	Collaborate with the team on application development tasks. Provide updates on progress and raise any technical concerns.	Team Collaboration Platform: Primary mode of communication for task assignments, progress updates, and technical discussions.	Daily stand-up meetings. Ad hoc communication as required for task coordination and issue resolution.	Team Collaboration Platform: Discussions, task updates, and file sharing. Daily Stand-up Meetings: Brief updates on progress, challenges, and plans for the day.	Jalal can escalate any significant technical issues or concerns to the Project Manager (Dana Hussain) or the Technical Lead for assistance	Jalal Ali: Actively participate in team meetings, provide updates on application development, and communicate any technical concerns promptly.	Feedback from Jalal regarding the effectiveness of communication channels and opportunities for improvement.	JalalAli@gmail.com
Abdulrahman Ahmed (Team Member - Testing-Application)	Collaborate with the team on application testing tasks. Provide updates on testing progress, bug reports, and test results.	Team Collaboration Platform: Primary mode of communication for testing-related tasks, updates, and discussions.	Regular testing meetings. Ad hoc communication as required for test coordination and bug resolution.	Team Collaboration Platform: Discussions, task updates, and file sharing. Testing Meetings: Detailed updates on testing progress, bug reports, and test results.	Abdulrahman can escalate any significant testing issues or concerns to the Project Manager (Dana Hussain) or the Testing Lead for assistance.	Abdulrahman Ahmed: Actively participate in testing meetings, provide updates on testing progress, and communicate any testing-related concerns promptly.	Feedback from Abdulrahman regarding the effectiveness of communication channels and opportunities for improvement.	AbdulrahmanAhmed@gmail.com
Shaikha Hamad (Head of Department - Monitoring and Controlling)	Monitor project progress and milestones. Address escalated issues and provide guidance on monitoring and controlling activities	Email: Primary mode of communication for department-related updates, monitoring progress, and addressing escalated issues.	Monthly updates on project monitoring and controlling. Ad hoc communication as required for urgent matters or stakeholder requests.	Monthly Monitoring and Controlling Reports: Detailed reports on project progress, challenges, and recommendations. Email Updates: Regular email updates on monitoring and controlling activities, upcoming milestones, and any urgent information.	Shaikha Hamad can be involved in escalated matters or decisions that require the Head of Department's attention and approval.	Shaikha Hamad: Review project monitoring and controlling updates, provide guidance, and make informed decisions	Feedback from Shaikha Hamad regarding the effectiveness of communication channels and their alignment with departmental objectives.	ShaikhaHamad@gmail.com
Bader Hassan (Coordinator)	Coordinate project activities. Provide updates on task assignments and progress.	Team Collaboration Platform: Primary mode of communication for coordination, task assignments, and progress updates.	Regular coordination meetings. Ad hoc communication as required for task coordination and issue resolution.	Team Collaboration Platform: Discussions, task updates, and file sharing. Coordination Meetings: Detailed updates on task assignments	Bader can escalate any significant project-related issues or concerns to the Project Manager (Dana Hussain) for assistance or further escalation to higher levels if necessary	Bader Hassan: Actively participate in team meetings, provide updates on project progress, communicate task assignments, and ensure effective communication between team members.	Feedback from Bader regarding the effectiveness of communication channels, team collaboration, and opportunities for improvement.	FaisalMohamed@gmail.com

-10-
Lesson
Learned

Lesson Learned :

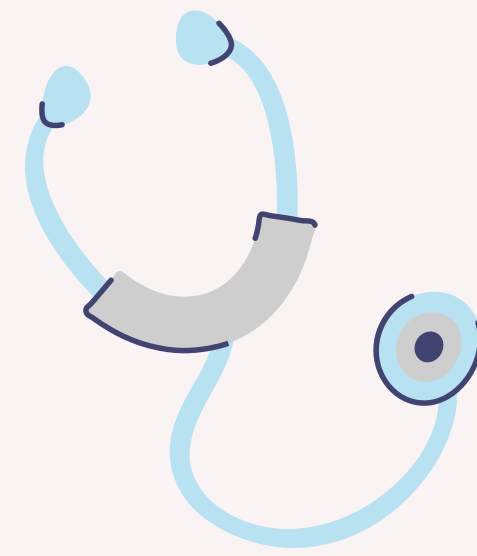

Dana
Hussain



To achieve a successful project, it's crucial to understand and respect each stakeholder's rights and obligations. Distributing tasks and responsibilities effectively fosters a cooperative team. Utilizing project management tools like Gantt charts and Microsoft Project is essential for project planning, timeline visualization, task dependencies, resource allocation, progress tracking, communication, and collaboration.

Lesson Learned :

Aijazi
Ali



Every project involves risks and problems, which project managers must anticipate and identify before beginning work. Risks can arise at any stage of the project, whether in the short or long term, and the impacts can vary. As project managers, we must be ready to handle these risks effectively. This includes managing risks as they arise and reducing the possibility of their occurrence. By proactively addressing potential risks, we can boost our chances of success.


Lesson Learned:

Noora
Abdulrahman



As a beginner project manager, I initially struggled with creating an effective Work Breakdown Structure (WBS) due to a lack of knowledge and experience. I faced challenges in defining the project scope, organizing tasks hierarchically, and determining the appropriate level of detail. Therefore, I learned to break down the project work optimally, ensuring better control and visibility over project execution.

Lesson Learned:

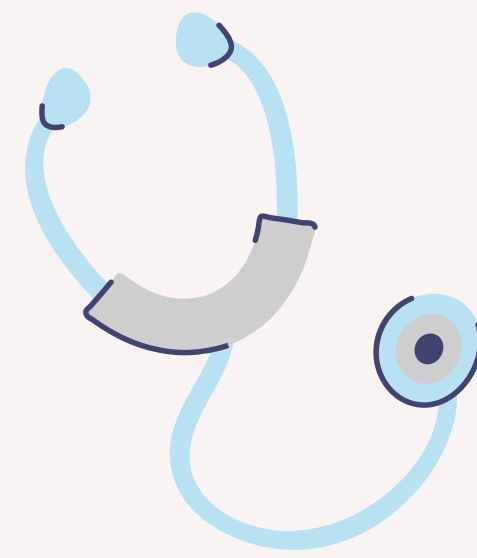

Manar
Hussain



I learned the importance of thorough scoping and stakeholder involvement in generating cost estimates, which helped set realistic budgets and ensured they stayed calibrated to changing needs. In addition, regularly revisiting estimates and comparing estimates to actual costs improved skills.

Thanks!
Any Questions?

