

ITIS 266

Project Management


Part 2

Dana Hussain Alhayki – 202203431
Aljazi Ali Almujaaddam – 202202227
Noora Abdulrahman Bumajaid -202203245
Manar Hussain Abdulrahim – 202201554

Group 05
Sec 02

Project organization:

Team Structure & Roles:

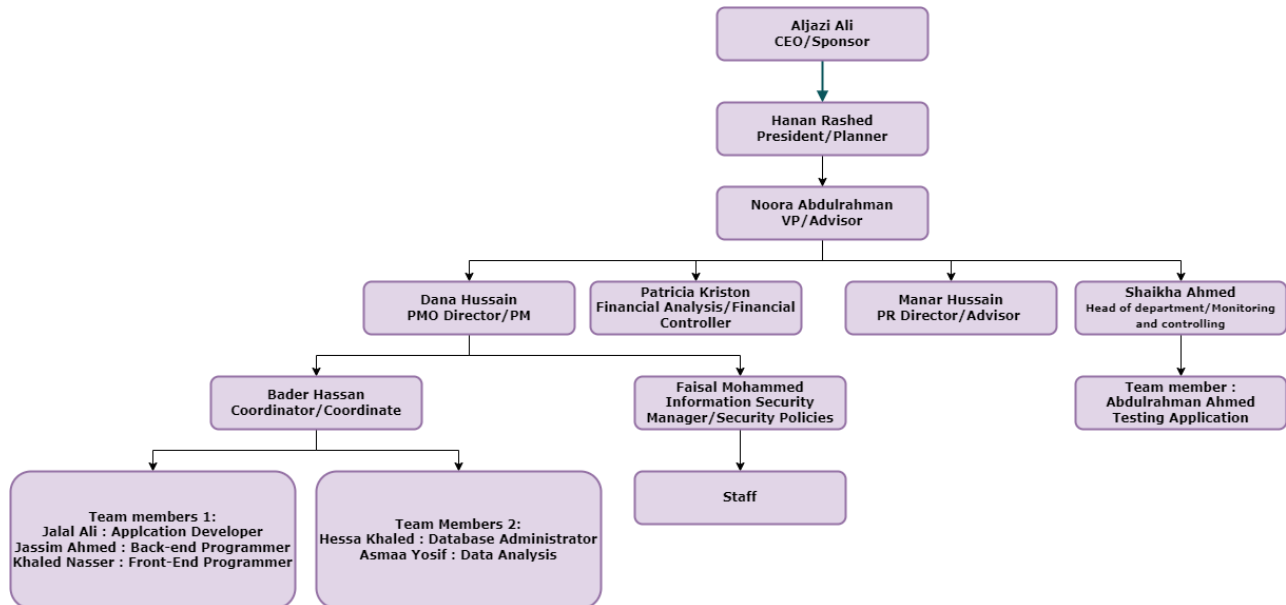

Responsibility Table:


Position	Responsibility
1.CEO/Sponsor	-Provides overall strategic direction and vision for the project. - Acts as the primary sponsor and advocate for the project. - Approves project goals, objectives, and major deliverables.
2. Planner /President	- Develops project plans and schedules. - Identifies project milestones and deliverables. - Coordinates with the project manager and team to ensure timely execution.
3. Vice President/Advisor	-Provides expert advice and guidance on project-related matters. -Assists in developing project strategies and plans. -Evaluates project risks and advises on risk mitigation strategies.

4. Project Manager /PMO Director	- Responsible for overall project management, planning, and coordination. - Acts as the main point of contact for the project team and stakeholders. - Manages project scope, schedule, and budget. - Ensures project objectives are met and delivers successful outcomes.
5. Financial Controller	- Provides financial analysis and oversight for the project. - Manages project budgeting and financial reporting. - Monitors project expenses and ensures financial compliance. - Collaborates with the project manager to make informed financial decisions.
6. Advisor /PR Director and Vice President	- Provides guidance and expertise related to public relations and strategic planning. - Assists in developing project communication strategies and stakeholder engagement. - Offers advice on project direction, goals, and decision-making.
7. Monitoring and Controlling /Head Of Department	- Monitors project progress, performance, and compliance. - Implements controls and processes to ensure project objectives are achieved. - Identifies and mitigates project risks and issues.
8. Coordinator	- Assists in coordinating project activities and resources. - Supports the project manager in administrative tasks. - Communicates and collaborates with team members and stakeholders.
9. Information Security Manager	- Develops and implements project security policies and procedures. - Ensures compliance with data protection regulations. - Manages project security risks and safeguards project assets.

10. Testing-Application	Conducts testing and quality assurance activities for project applications. - Develops test plans and executes test cases. - Reports and tracks defects, working with the development team to resolve issues
11. Application Developer	Develops and maintains project applications and software solutions. - Collaborates with the project team to understand requirements and implement solutions. - Conducts testing and debugging to ensure application functionality
12. Backend Programmer	- Responsible for developing and maintaining the backend systems and infrastructure. - Collaborates with frontend programmers and other team members to integrate systems. - Ensures the backend functionality aligns with project requirements.
13. Frontend Programmer	Develops and maintains the user interface and frontend components of the project. - Collaborates with backend programmers and other team members for seamless integration. - Implements user experience (UX) design and ensures responsive and intuitive interfaces.
14. Database Administrator	- Manages the project's databases and data storage systems. - Ensures data integrity, security, and availability. - Optimizes database performance and troubleshoots issues.
15. Data Analyst	- Conducts data analysis and provides insights for decision-making. - Cleans and analyzes project data to identify trends, patterns, and opportunities. - Collaborates with the project team to optimize data-driven strategies.

Work breakdown structure (WBS):

Work Breakdown Structure (chart Form):

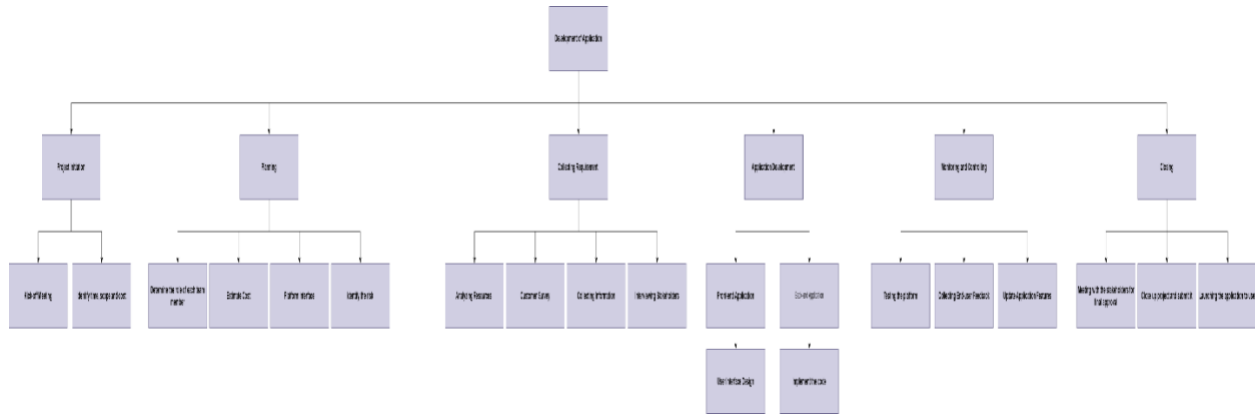

Work Breakdown Structure (Tabular Form):

	WBS	Task Mode	Task Name	Duration	Start	Finish	Predecessors
1	1	🚀	Project Begin	0 days	Wed 1/1/25	Wed 1/1/25	
2	2	🚀	Project Initiation	1 day?	Wed 1/1/25	Wed 1/1/25	
3	2.1	🚀	Kick-off Meeting	1 day	Wed 1/1/25	Wed 1/1/25	
4	2.2	🚀	Identify time, scope and cost	1 day	Wed 1/1/25	Wed 1/1/25	1
5	3	🚀	Planning	5 days	Fri 1/3/25	Thu 1/9/25	2
6	3.1	🚀	Determine the role of each team member	1 day	Fri 1/3/25	Fri 1/3/25	
7	3.2	🚀	Platform Interface	2 days	Sat 1/4/25	Sun 1/5/25	
8	3.3	🚀	Estimate Cost	2 days	Mon 1/6/25	Tue 1/7/25	
9	3.4	🚀	Identify the risk	2 days	Wed 1/8/25	Thu 1/9/25	
10	4	🚀	Collecting Requirements	12 days	Fri 1/10/25	Mon 1/27/25	2,5
11	4.1	🚀	Interviewing Stakeholders	2 days	Fri 1/10/25	Sun 1/12/25	
12	4.2	🚀	Collecting Information	5 days	Mon 1/13/25	Fri 1/17/25	11
13	4.3	🚀	Customer Survey	3 days	Sat 1/18/25	Tue 1/21/25	
14	4.4	🚀	Analyzing Resources	4 days	Wed 1/22/25	Mon 1/27/25	11,12,13
15	5	🚀	Application Development	166 days	Mon 2/3/25	Mon 9/22/25	14
16	5.1	🚀	Front-end Application	67 days	Mon 2/3/25	Tue 5/6/25	
17	5.1.1	🚀	User Interface Design	67 days	Mon 2/3/25	Tue 5/6/25	
18	5.2	🚀	Back-end Application	98 days	Thu 5/8/25	Mon 9/22/25	16
19	5.2.1	🚀	Implement the code	98 days	Thu 5/8/25	Mon 9/22/25	
20	6	🚀	Monitoring and Controlling	59 days	Thu 9/25/25	Tue 12/16/25	19
21	6.1	🚀	Testing the platform	19 days	Thu 9/25/25	Tue 10/21/25	
22	6.2	🚀	Collecting End-user Feedback	6 days	Tue 10/21/25	Tue 10/28/25	

	WBS	Task Mode	Task Name	Duration	Start	Finish	Predecessors
22	6.2	🚀	Collecting End-user Feedback	6 days	Tue 10/21/25	Tue 10/28/25	
23	6.3	🚀	Update Application	35 days	Wed 10/29/25	Tue 12/16/25	21,22
24	7	🚀	Closing	11 days	Thu 12/18/25	Thu 1/1/26	15,23
25	7.1	🚀	Meeting with the stakeholders for final approval	3 days	Thu 12/18/25	Sun 12/21/25	
26	7.2	🚀	Close up project and submit it	1 day	Mon 12/22/25	Mon 12/22/25	25
27	7.3	🚀	Launching the application to	6 days	Thu 12/25/25	Thu 1/1/26	
28	7.4	🚀	Project Closure	0 days	Thu 1/1/26	Thu 1/1/26	

Gantt Chart:


GANTT CHART

	WBS ▾		Task Mode ▾	Task Name ▾	Duration ▾	Start ▾	Finish ▾	Predecessors ▾
1	1			Project Begin	0 days	Wed 1/1/25	Wed 1/1/25	
2	2			▾ Project Initiation	1 day?	Wed 1/1/25	Wed 1/1/25	
3	2.1			Kick-off Meeting	1 day	Wed 1/1/25	Wed 1/1/25	
4	2.2			Identify time, scope and cost	1 day	Wed 1/1/25	Wed 1/1/25	1
5	3			▾ Planning	5 days	Fri 1/3/25	Thu 1/9/25	2
6	3.1			Determine the role of each team member	1 day	Fri 1/3/25	Fri 1/3/25	
7	3.2			Platform Interface	2 days	Sat 1/4/25	Sun 1/5/25	
8	3.3			Estimate Cost	2 days	Mon 1/6/25	Tue 1/7/25	
9	3.4			Identify the risk	2 days	Wed 1/8/25	Thu 1/9/25	
10	4			▾ Collecting Requirements	12 days	Fri 1/10/25	Mon 1/27/25	2,5
11	4.1			Interviewing Stakeholders	2 days	Fri 1/10/25	Sun 1/12/25	
12	4.2			Collecting Information	5 days	Mon 1/13/25	Fri 1/17/25	11
13	4.3			Customer Survey	3 days	Sat 1/18/25	Tue 1/21/25	
14	4.4			Analyzing Resources	4 days	Wed 1/22/25	Mon 1/27/25	11,12,13
15	5			▾ Application Development	166 days	Mon 2/3/25	Mon 9/22/25	14
16	5.1			▾ Front-end Application	67 days	Mon 2/3/25	Tue 5/6/25	
17	5.1.1			User Interface Design	67 days	Mon 2/3/25	Tue 5/6/25	
18	5.2			▾ Back-end Application	98 days	Thu 5/8/25	Mon 9/22/25	16
19	5.2.1			Implement the code	98 days	Thu 5/8/25	Mon 9/22/25	
20	6			▾ Monitoring and Controlling	59 days	Thu 9/25/25	Tue 12/16/25	19
21	6.1			Testing the platform	19 days	Thu 9/25/25	Tue 10/21/25	
22	6.2			Collecting End-user Feedback	6 days	Tue 10/21/25	Tue 10/28/25	

	WBS ▼	 Task Mode ▼	Task Name ▼	Duration ▼	Start ▼	Finish ▼	Predecessors ▼
22	6.2		Collecting End-user Feedback	6 days	Tue 10/21/25	Tue 10/28/25	
23	6.3		Update Application	35 days	Wed 10/29/25	Tue 12/16/25	21,22
24	7		▲ Closing	11 days	Thu 12/18/25	Thu 1/1/26	15,23
25	7.1		Meeting with the stakeholders for final approval	3 days	Thu 12/18/25	Sun 12/21/25	
26	7.2		Close up project and submit it	1 day	Mon 12/22/25	Mon 12/22/25	25
27	7.3		Launching the application to	6 days	Thu 12/25/25	Thu 1/1/26	
28	7.4		Project Closure	0 days	Thu 1/1/26	Thu 1/1/26	

December 21			February 11			April 1			May 21			July 11			September 1			October 21			Decem
12/8	12/29	1/19	2/9	3/2	3/23	4/13	5/4	5/25	6/15	7/6	7/27	8/17	9/7	9/28	10/19	11/9	11/30	1			

1/1

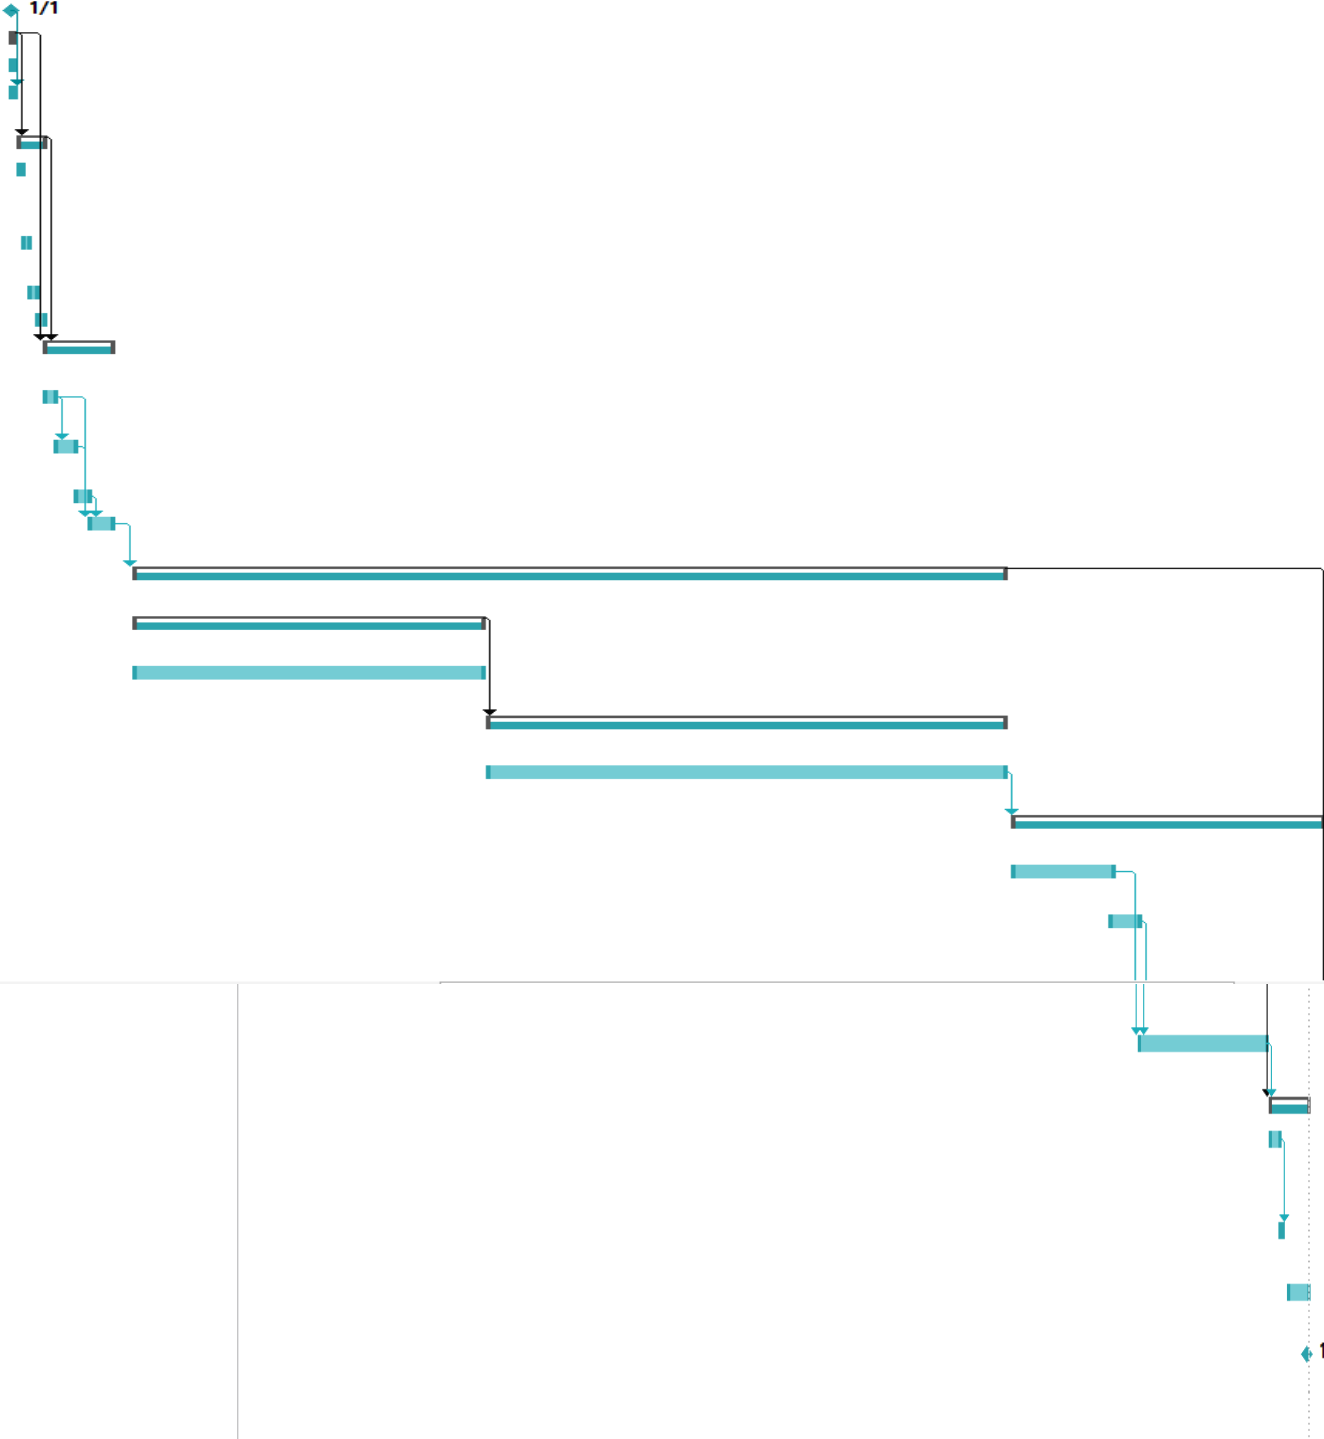

Cost Estimate:

	#Units/Hrs.	Cost/Units/Hrs.	Subtotals	WBS level 1 Totals	% Of total
1 Project Initiation				\$800	0.04%
1.1 Kick-off Meeting	3	\$200	\$600		
1.2 Identify time, scope, and cost	4	\$50	\$200		
2 Planning				\$76,500	3.825%
2.1 Determine the role of each team member	5	\$100	\$500		
2.2 Platform Interface	16	\$2,000	\$32,000		
2.3 Estimate Cost	10	\$2,000	\$20,000		
2.4 Identify the risk	12	\$2,000	\$24,000		
3 Collecting Requirements				\$24,400	1.22%
3.1 Interviewing Stakeholders	8	\$200	\$1,600		
3.2 Collecting Information	32	\$300	\$9,600		
3.3 Customer Survey	24	\$50	\$1,200		
3.4 Analyzing Resources	30	\$400	\$12,000		
4 Application Development				\$1,020,000	51%
4.1 Front-end Application				\$300,000	
4.1.1 User Interface Design	500	\$600	\$300,000		
4.2 Back-end Application				\$720,000	
4.2.1 Implement the code	720	\$1,000	\$720,000		
5 Monitoring and Controlling				\$32,350	1.6175%
5.1 Testing the platform	120	\$100	\$12,000		
5.2 Collecting End-user Feedback	40	\$40	\$1,600		
5.3 Update Application Features	250	\$75	\$18,750		
6 Closing				\$83,240	4.162%
6.1 Meeting with the stakeholders for final approval	15	\$200	\$3,000		
6.2 Close up project and submit it	8	\$30	\$240		
6.3 Launching the application to user	40	\$2,000	\$80,000		
6.4 Project Closure					
Reserves				\$762,710	38.1355%
Total Project Cost Estimate				\$1,237,290	61.8645%

Risk management plan:

Risk Register:

No.	Rank	Risk	Description	Category	Root Cause	Triggers	Potential Responses	Risk Owner	Probability	Impact	Status
R1	1	Work Ethics	Ethical issues related to work practice or behaviour	Organizational	Lack of clear ethical guidelines or enforcements	Unethical behavior by employees	Establish and enforce clear ethical guidelines, provide ethics training	Human Resources	Medium	High	Ongoing
R2	2	Security and Privacy Issues	Breaches of security and privacy of user data	Technical	Inadequate security measures or vulnerabilities	Hacking attempts, data leaks	Strengthen security measures, implement encryption and access controls	IT Departmentt	Low	High	Mitigated
R3	3	Lack of Quality of Care and Limited Diagnosis	Insufficient quality of care and limited diagnostic capabilities	Operational	Inadequate training or resources for healthcare professionals	Misdiagnosis, inadequate treatment	Improve training programs, invest in advanced diagnostic tools	Healthcare Management	High	Medium	In progress
R4	4	Low Adaption of using the Application	Limited user adaption and engagement with the application	Organizational	Lack of awareness or understanding of the benefits	Resistance to change, lack of user-friendly interface	Conduct awareness campaigns, improve user interface and user experience	Marketing Department	Medium	Medium	Ongoing
R5	5	Technical Issues or System Failures	Malfunctions of failures in the application or system	Technical	Software bugs, hardware failures	Application crashes, system downtime	Regular maintenance, bug fixing, backup systems	IT Department	High	High	Open
R5	6	Integration Issues	Challenges in integrating the application with existing systems	Technical	Incompatibility with legacy systems, lack of interoperability	Data synchronization issues and data loss	Conduct compatibility assessments, develop integration protocols	IT Department	Low	Medium	Resolved

Risk Matrix:

probability	High		Risk 3 - Lack of Quality of Care and Limited Diagnosis	Risk 5 - Technical Issues or System Failures
	medium		Risk 4 - Low Adaption of using the Application	Risk 1 - Work Ethics
	Low		Risk 6 - Integration Issues	Risk 2 - Security and Privacy Issues
		Low	Medium	High
		impact		

Communication Management Plan:

Stakeholder Identification	Communication Objectives	Communication Channel	Communication Frequency	Communication Methods	Escalation procedure	Communication Responsibilities	Communication Evaluation	Contact Information
Aljazi Ali (Sponsor)	- Provide project vision and strategic guidance. - Stay informed about project progress and milestones. - Address escalated issues and make key decisions.	Email: Primary mode of communication for high-level project updates, strategic guidance, and addressing escalated issues.	- Monthly updates on project status and achievements. - Ad hoc communication as required for urgent matters or stakeholder requests	- Monthly Project Updates: Detailed reports highlighting project achievements, challenges, and upcoming milestones. - One-on-One Meetings: Scheduled meetings to discuss project progress, address concerns, and seek strategic input.	Aljazi Ali can escalate any significant project-related issues or concerns to the Project Manager (Dana Hussain) or involve higher-level stakeholders, such as the President (Hanan Rashed).	Review project updates, provide strategic guidance, and make informed decisions.	The effectiveness of communication channels and their alignment with strategic objectives	202202227@stu.uob.edu.lb
Dana Hussain (Project Manager)	- Facilitate effective communication among all stakeholders. - Share project progress, updates, and milestones. - Address and resolve issues raised by stakeholders.	Email: Primary mode of communication for project updates, reports, and addressing stakeholder concerns.	- Weekly project team meetings. - Monthly stakeholder updates. - Ad hoc communication as required to address urgent matters or specific stakeholder requests.	- Project Team Meetings: Weekly meetings to discuss progress, address issues, and assign tasks. - Stakeholder Updates: Monthly reports highlighting project status, achievements, and upcoming activities. - Ad hoc Communication: Additional meetings or communications as required to address urgent matters or specific stakeholder requests.	- If any stakeholder has an issue or concern that cannot be resolved at the project team level, they can escalate it to Dana Hussain. - Dana will review the issue, involve relevant stakeholders, and work towards resolving it in a timely manner. - If the issue remains unresolved, Dana will escalate it to the Project Sponsor (Aljazi Ali) for further action and decision-making.	Responsible for overall communication management, including preparing and disseminating project updates, conducting meetings, and addressing stakeholder concerns.	Feedback from stakeholders regarding the effectiveness of communication channels and Dana's communication approach.	202203431@stu.uob.edu.lb
Patricia Kriston (Financial Controller)	- Share financial analysis reports and updates. - Discuss budgetary matters and financial forecasts. - Address any financial concerns or queries.	Email: The primary mode of communication for formal project updates, reports, and financial-related discussions.	- Monthly financial reports and updates. - Ad hoc communication as required or for urgent financial matters.	- Formal Financial Reports: Detailed reports on financial analysis, budget status, and forecasts. - Email Updates: Regular email updates on financial matters and any urgent financial-related information.	If Patricia encounters any financial issues or requires additional support, she can escalate them to the Project Manager (Dana Hussain) or the Project Sponsor (Aljazi Ali) for assistance.	Actively participate in project meetings, provide input on financial matters, and communicate any concerns promptly.	The effectiveness of financial communication channels and opportunities for improvement.	PatriciaKriston@gmail.com
Manar Hussain (PR Director)	- Share PR strategies and updates. - Coordinate PR campaigns and activities. - Address any PR-related concerns or queries.	Email: Primary mode of communication for PR-related updates, campaigns, and coordination.	- Monthly PR updates. - Ad hoc communication as required for urgent PR matters.	- PR Campaign Reports: Detailed reports on PR campaigns, media coverage, and public perception. - Email Updates: Regular email updates on PR activities, upcoming events, and any urgent PR-related information.	If Manar encounters any significant PR issues or requires additional support, she can escalate them to the Project Manager (Dana Hussain) or the Project Sponsor (Aljazi Ali) for assistance.	Actively participate in project meetings, provide input on PR matters, and communicate any concerns or updates promptly.	The effectiveness of PR communication channels and opportunities for improvement.	202201554@stu.uob.edu.lb
Noora Abdulrahman (Vice President)	- Provide strategic guidance and input. - Stay informed about project progress and milestones. - Address escalated issues and make key decisions.	Email: Primary mode of communication for high-level project updates, strategic guidance, and addressing escalated issues.	- Monthly updates on project status and achievements. - Ad hoc communication as required for urgent matters or stakeholder requests.	- Monthly Project Updates: Detailed reports highlighting project achievements, challenges, and upcoming milestones. - One-on-One Meetings: Scheduled meetings to discuss project progress, address concerns, and seek strategic input.	Escalate any significant project-related issues or concerns to the Project Manager (Dana Hussain) or involve higher-level stakeholders, such as the President (Hanan Rashed).	Review project updates, provide strategic guidance, and make informed decisions.	Regarding the effectiveness of communication channels and their alignment with strategic objectives.	202203241@stu.uob.edu.lb
Hanan Rashed (President)	- Provide overall project direction and leadership. - Stay informed about project progress and achievements. - Address escalated issues and make key decisions.	Email: Primary mode of communication for high-level project updates, strategic guidance, and addressing escalated issues.	Monthly updates on project status and achievements.	- Monthly Project Updates: Detailed reports highlighting project achievements, challenges, and upcoming milestones. - One-on-One Meetings: Scheduled meetings to discuss project progress, address concerns, and seek strategic input.	Hanan Rashed can be involved in escalated matters or decisions that require the President's attention and approval.	Hanan Rashed: Review project updates, provide strategic guidance, and make informed decisions.	Feedback from Hanan Rashed regarding the effectiveness of communication channels and their alignment with strategic objectives.	HananRashed@gmail.com
Jassim Ahmed (Team Member - Backend Programmer)	- Collaborate with the team on backend development tasks. - Provide updates on progress and raise any technical concerns.	Team Collaboration Platform: Primary mode of communication for task assignments, progress updates, and technical discussions.	Daily stand-up meetings. Ad hoc communication as required for task coordination and issue resolution.	- Team Collaboration Platform: Discussions, task updates, and file sharing. - Daily Stand-up Meetings: Brief updates on progress, challenges, and plans for the day.	Jassim can escalate any significant technical issues or concerns to the Project Manager (Dana Hussain) or the Technical Lead (Jalal Ali) for assistance.	Jassim Ahmed: Actively participate in team meetings, provide updates on backend development, and communicate any technical concerns promptly.	Feedback from Jassim regarding the effectiveness of communication channels and opportunities for improvement.	JassimAhmed@gmail.com
Khaled Nasser (Team Member - Frontend Programmer)	- Collaborate with the team on frontend development tasks. - Provide updates on progress and raise any technical concerns.	Team Collaboration Platform: Primary mode of communication for task assignments, progress updates, and technical discussions.	Daily stand-up meetings. Ad hoc communication as required for task coordination and issue resolution.	- Team Collaboration Platform: Discussions, task updates, and file sharing. - Daily Stand-up Meetings: Brief updates on progress, challenges, and plans for the day.	Khaled can escalate any significant technical issues or concerns to the Project Manager (Dana Hussain) or the Technical Lead (Jalal Ali) for assistance.	Khaled Nasser: Actively participate in team meetings, provide updates on frontend development, and communicate any technical concerns promptly.	Feedback from Khaled regarding the effectiveness of communication channels and opportunities for improvement.	KhaledNasser@gmail.com
Asmaa Yousif (Team Member - Data Analysis)	- Collaborate with the team on data analysis tasks. - Provide updates on analysis progress and insights.	Team Collaboration Platform: Primary mode of communication for task assignments, data analysis updates, and discussions.	Weekly data analysis meetings. Ad hoc communication as required for task coordination and data-related discussions.	- Team Collaboration Platform: Discussions, task updates, and file sharing. - Weekly Data Analysis Meetings: Detailed updates on analysis progress, findings, and challenges.	Asmaa can escalate any significant data analysis issues or concerns to the Project Manager (Dana Hussain) or the Data Analysis Lead for assistance.	Asmaa Yousif: Actively participate in data analysis meetings, provide updates on analysis progress, and communicate any data-related concerns promptly.	Feedback from Asmaa regarding the effectiveness of communication channels and opportunities for improvement.	AsmaaYousif@gmail.com
Hessa Khaled (Team Member - Database Administrator)	- Collaborate with the team on database administration tasks. - Provide updates on database configurations and maintenance.	Team Collaboration Platform: Primary mode of communication for database-related tasks, updates, and discussions.	Weekly database administration meetings. Ad hoc communication as required for task coordination and database-related discussions.	- Team Collaboration Platform: Discussions, task updates, and file sharing. - Weekly Database Administration Meetings: Detailed updates on database configurations, maintenance, and challenges.	Hessa can escalate any significant database administration issues or concerns to the Project Manager (Dana Hussain) or the Database Administration Lead for assistance.	Hessa Khaled: Actively participate in database administration meetings, provide updates on database tasks, and communicate any database-related concerns promptly.	Feedback from Hessa regarding the effectiveness of communication channels and opportunities for improvement.	HessaKhaled@gmail.com
Jalal Ali (Team Member - Application Developer)	- Collaborate with the team on application development tasks. - Provide updates on progress and raise any technical concerns.	Team Collaboration Platform: Primary mode of communication for task assignments, progress updates, and technical discussions.	Daily stand-up meetings. Ad hoc communication as required for task coordination and issue resolution.	- Team Collaboration Platform: Discussions, task updates, and file sharing. - Daily Stand-up Meetings: Brief updates on progress, challenges, and plans for the day.	Jalal can escalate any significant technical issues or concerns to the Project Manager (Dana Hussain) or the Technical Lead for assistance.	Jalal Ali: Actively participate in team meetings, provide updates on application development, and communicate any technical concerns promptly.	Feedback from Jalal regarding the effectiveness of communication channels and opportunities for improvement.	JalalAli@gmail.com
Abdulrahman Ahmed (Team Member - Testing-Application)	- Collaborate with the team on application testing tasks. - Provide updates on testing progress, bug reports, and test results.	Team Collaboration Platform: Primary mode of communication for testing-related tasks, updates, and discussions.	Regular testing meetings. Ad hoc communication as required for test coordination and bug resolution.	- Team Collaboration Platform: Discussions, task updates, and file sharing. - Testing Meetings: Detailed updates on testing progress, bug reports, and test results.	Abdulrahman can escalate any significant testing issues or concerns to the Project Manager (Dana Hussain) or the Testing Lead for assistance.	Abdulrahman Ahmed: Actively participate in testing meetings, provide updates on testing progress, and communicate any testing-related concerns promptly.	Feedback from Abdulrahman regarding the effectiveness of communication channels and opportunities for improvement.	AbdulrahmanAhmed@gmail.com
Shaikha Hamad (Head of Department - Monitoring and Controlling)	- Monitor project progress and milestones. - Address escalated issues and provide guidance on monitoring and controlling activities.	Email: Primary mode of communication for department-related updates, monitoring progress, and addressing escalated issues.	Monthly updates on project monitoring and controlling. Ad hoc communication as required for urgent matters or stakeholder requests.	- Monthly Monitoring and Controlling Reports: Detailed reports on project progress, challenges, and recommendations. - Email Updates: Regular email updates on monitoring and controlling activities, upcoming milestones, and any urgent information.	Shaikha Hamad can be involved in escalated matters or decisions that require the Head of Department's attention and approval.	Shaikha Hamad: Review project monitoring and controlling updates, provide guidance, and make informed decisions.	Feedback from Shaikha Hamad regarding the effectiveness of communication channels and their alignment with departmental objectives.	ShaikhaHamad@gmail.com
Bader Hassan (Coordinator)	- Coordinate project activities. - Provide updates on task assignments and progress.	Team Collaboration Platform: Primary mode of communication for coordination, task assignments, and progress updates.	Regular coordination meetings. Ad hoc communication as required for task coordination and issue resolution.	- Team Collaboration Platform: Discussions, task updates, and file sharing. - Coordination Meetings: Detailed updates on task assignments.	Bader can escalate any significant project-related issues or concerns to the Project Manager (Dana Hussain) or further escalation to higher levels if necessary.	Bader Hassan: Actively participate in team meetings, provide updates on project progress, communicate task assignments, and ensure effective communication between team members.	Feedback from Bader regarding the effectiveness of communication channels, team collaboration, and opportunities for improvement.	FaisalMohamed@gmail.com
